

# Huntsville MPO Project Update

**August 28, 2019**

# Church Street Phase I between Pratt Avenue and Monroe Street

Status: Under Construction and  
about 50% complete

Est. Cost \$12,846,798

Start Date: November 2018

Anticipated Completion Date: 2020



# Northern Bypass from Pulaski Pike to US Hwy 231/431



Status: Plans are 80% complete. ROW acquisition to be completed this year.

Est. Cost \$40,000,000

Anticipated Start Date: FY 2020

Anticipated Completion Date: FY 2022

# Martin Road between Zierdt Road and Laracy Drive



Status: Two separate projects that will be built in phases.

Phase I under construction (from Old Jim Williams Rd to Zierdt) with anticipated completion in Spring 2020

Phase II is scheduled for Spring 2020

Estimated Cost for both phases \$25,000,000

Phase I Start Date: July 2018

About 35% Complete

Phase I Completion Date: Spring 2020

# North Parkway at Mastin Lake Road

Status: Plans are 90% complete. Anticipate ROW to be completed this fall. A Clearing Project with Structure Removal and Utility Relocation will be bid this Fall.

Est. Cost \$42,600,000

Anticipated Overpass Project Start Date: Late 2020



# Access Management on US 231 between Weatherly Road and Hobbs Island Road

Status: Plans are 30% complete.  
Anticipate Public Involvement  
Meeting Fall 2019.


Est. Cost \$15,000,000

Anticipated Start Date: Summer  
2020

Anticipated Completion Date:  
Summer 2021



# Cecil Ashburn Drive Improvements

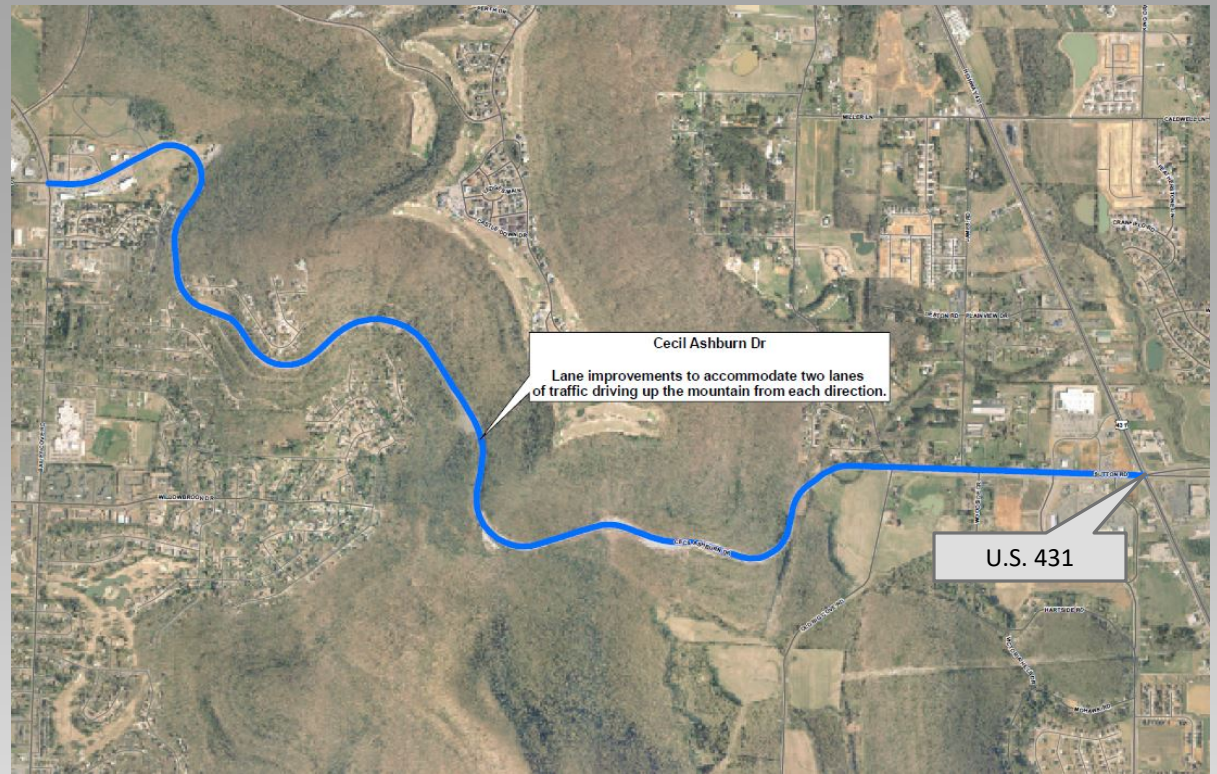

Status: The contractor is on schedule to have two lanes open by October 2019. There will be another 8-10 months after that before the entire project is complete.

Est. Cost \$22,000,000

# Winchester Road from Dominion to Naugher Road



Status: Plans are 90% complete. Right-of Way Acquisition began in 2017

Est. Cost \$15,500,000

Anticipated Start Date: Mid 2020

Anticipated Completion Date: Mid 2022

## ***SR 255 (Research Park Boulevard) Widening from US 72 to south of Old Madison Pike***


Estimated Cost \$23,415,000

Start Date: August 2019

Anticipated Completion Date: Late 2021



# US 72 West between Providence Main and County Line Road

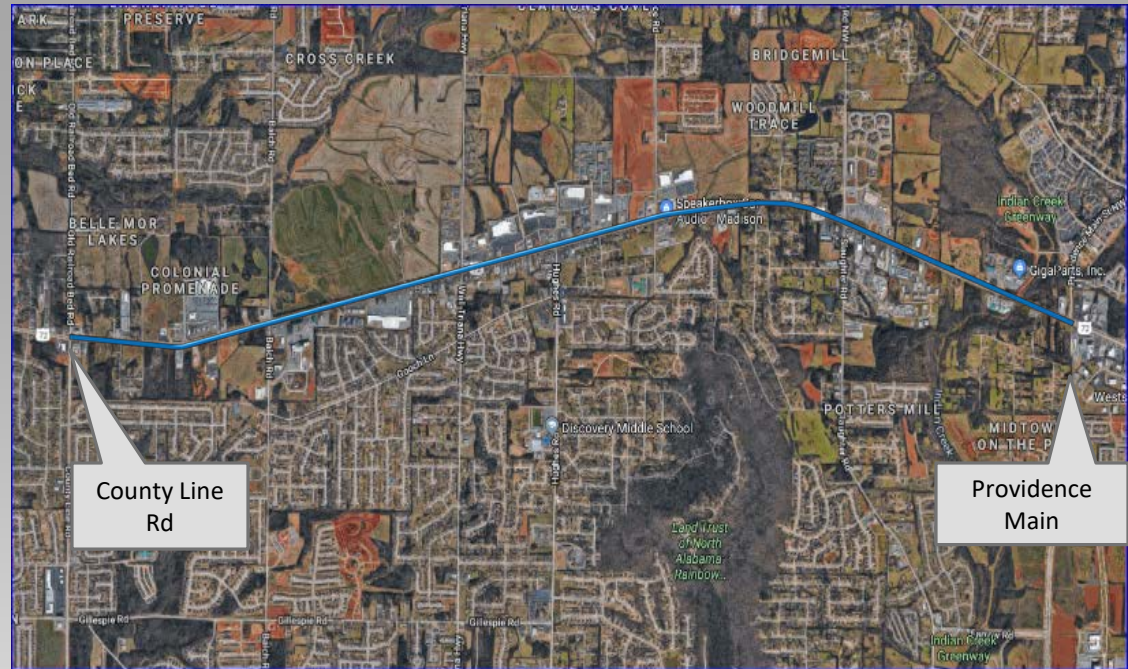

Status: Plans are 30% complete. Multiple funding sources and considering project phases due to budget. Right-of Way acquisition anticipated for Early 2021

Est. Cost \$60,000,000+

Anticipated Start Date: FY 2022

Anticipated Completion Date: FY 2024

# Zierdt Road between Madison Boulevard and Martin Road

Status: Four project phases. Work started in 2015. The last phase (Phase IV) is under contract

Est. Cost (Total) \$27,000,000

Work Started: Fall 2018

Anticipated Completion Date: Early 2021



# Winchester Road from Naugher Rd to Riverton Rd




Status: Under Construction and about 15% Complete

Cost \$6,597,823

Start Date: February 2019

Anticipated Completion Date: March 2020

# Interchange at Blake Bottom Rd and SR 255 (Research Park Blvd)

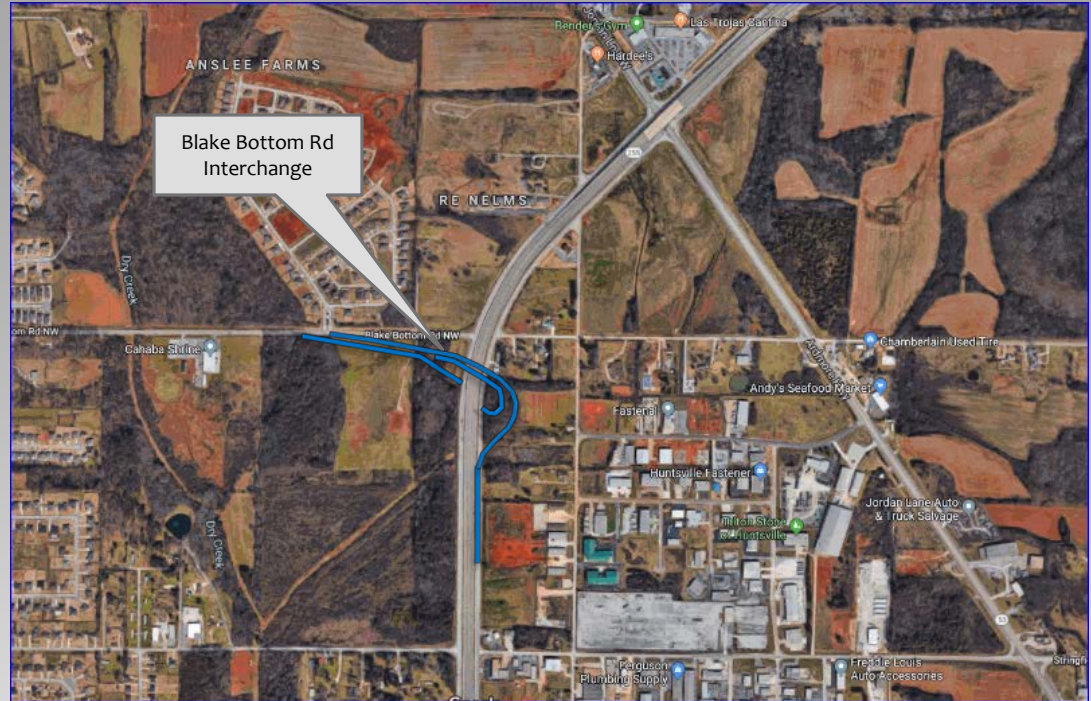

Status: Under Construction and about 80% Complete

Cost \$7,821,656

Start Date: November 2017

Anticipated Completion Date: Fall 2019

# Four Bridge Replacements on Old Hwy 431



Status: September 27, 2019 letting date

Cost \$13,500,000

# I-565 Interchange Improvements at Greenbrier Rd



Status: Under Construction and 50% complete

Cost \$10,264,000

Anticipated Completion Date: December 2019

# I-565 Additional Lanes from I-65 to County Line Rd


Status: Under Design

Projected Start Date: Spring 2020

Cost \$17,000,000



# Jeff Rd Additional Lanes from South of Capshaw Road to North of Douglas Rd

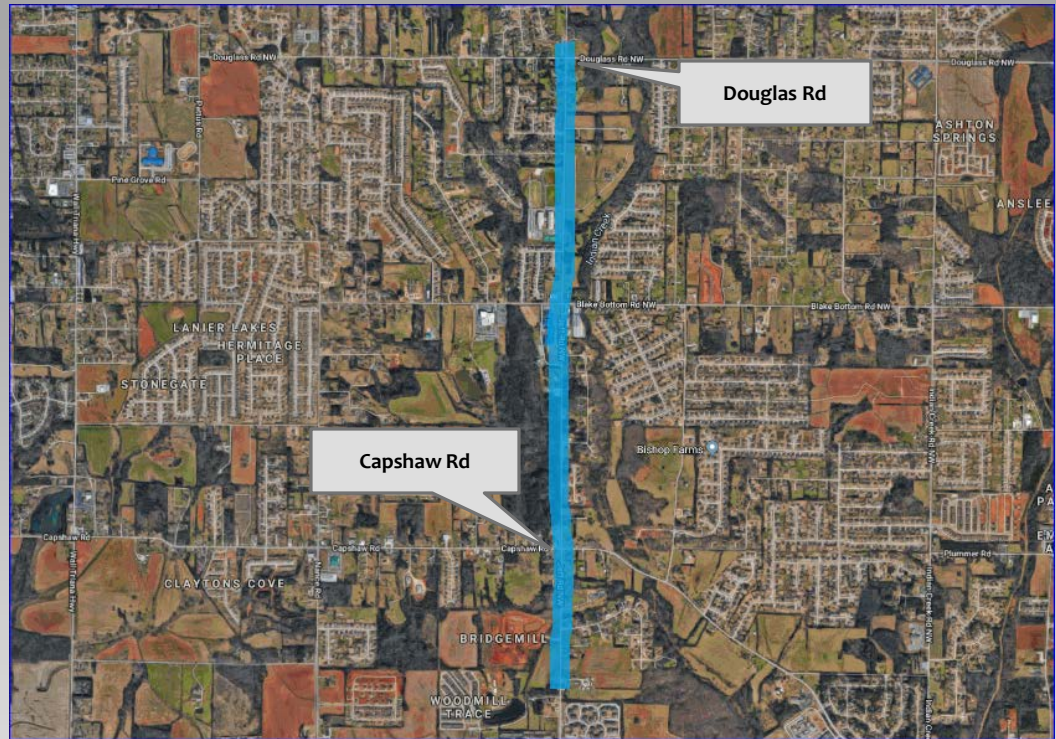

Status: Under Design

Projected Start Date: FY 2021

Cost \$13,500,000

## **Total Amount of Work in Design and Construction**

**\$352,045,277**
