

# Huntsville MPO Project Update

**April 22, 2020**

# Church Street Phase I between Pratt Avenue and Monroe Street

Status: Under Construction and  
about 55% complete

Est. Cost \$12,846,798

Start Date: November 2018

Anticipated Completion Date:  
Late Summer 2020



# Northern Bypass from Pulaski Pike to US Hwy 231/431



Status: Plans are 85% complete. ROW acquisition to be completed this year.

Est. Cost \$40,000,000

Anticipated Start Date: FY 2021

Anticipated Completion Date: FY 2022



# Martin Road between Zierdt Road and Laracy Drive



Status: Two separate projects that will be built in phases.

Phase I under construction (from Old Jim Williams Rd to Zierdt) with anticipated completion in Late Summer 2020

Phase II is scheduled for FY 2023

Estimated Cost for both phases \$25,000,000

Phase I Start Date: July 2018

About 40% Complete

Phase I Completion Date: Late Summer 2020

# North Parkway at Mastin Lake Road

Status: Plans are 90% complete. ROW acquisition to be completed this spring. A Clearing Project with Structure Removal will be bid this April 2020.

Est. Cost \$42,600,000

Anticipated Overpass Project Start Date: FY 2022






# Access Management on US 231 between Weatherly Road and Hobbs Island Road

Status: Plans are 30% complete.  
Anticipate Public Involvement Meeting Summer/Fall 2020.


Est. Cost \$15,000,000

Anticipated Start Date: Summer 2021

Anticipated Completion Date: Fall 2022

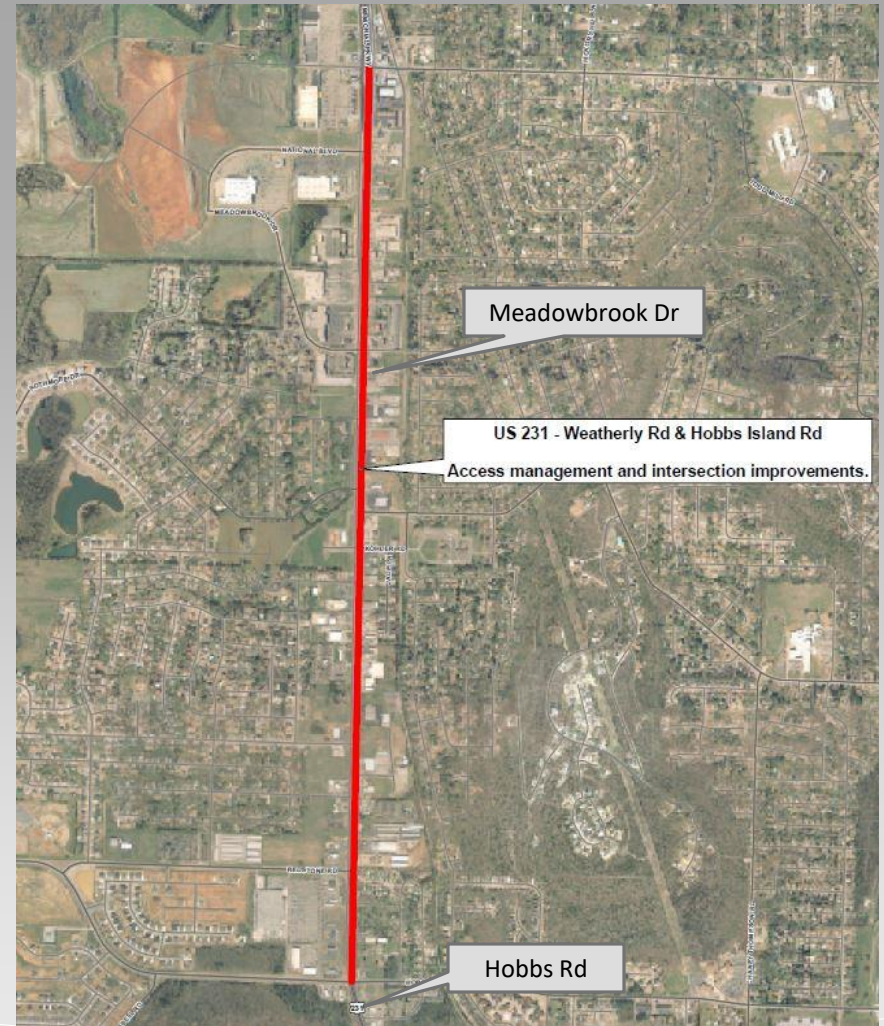

# Cecil Ashburn Drive Improvements

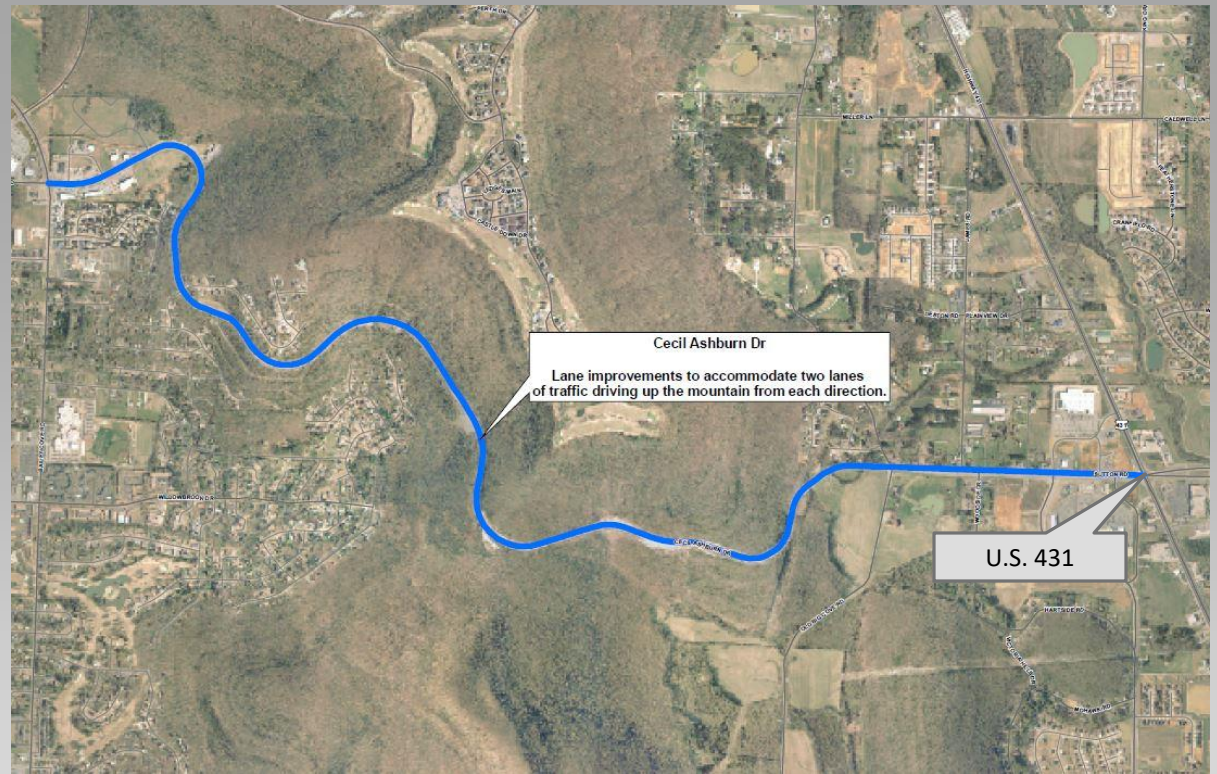

Status: The contractor completed two lanes in October 2019. There will be another 8-10 months after that before the entire project is complete.

Est. Cost \$22,000,000



# Winchester Road from Dominion to Naugher Road



Status: Plans are 90% complete. Right-of Way Acquisition began in 2017

Est. Cost \$15,500,000

Anticipated Start Date: FY 2021

Anticipated Completion Date: FY 2023



# ***SR 255 (Research Park Boulevard) Widening from US 72 to south of Old Madison Pike***


Estimated Cost \$23,415,000

Work started August 2019  
25% Complete

Anticipated Completion Date: Late 2021



# US 72 West between Providence Main and County Line Road

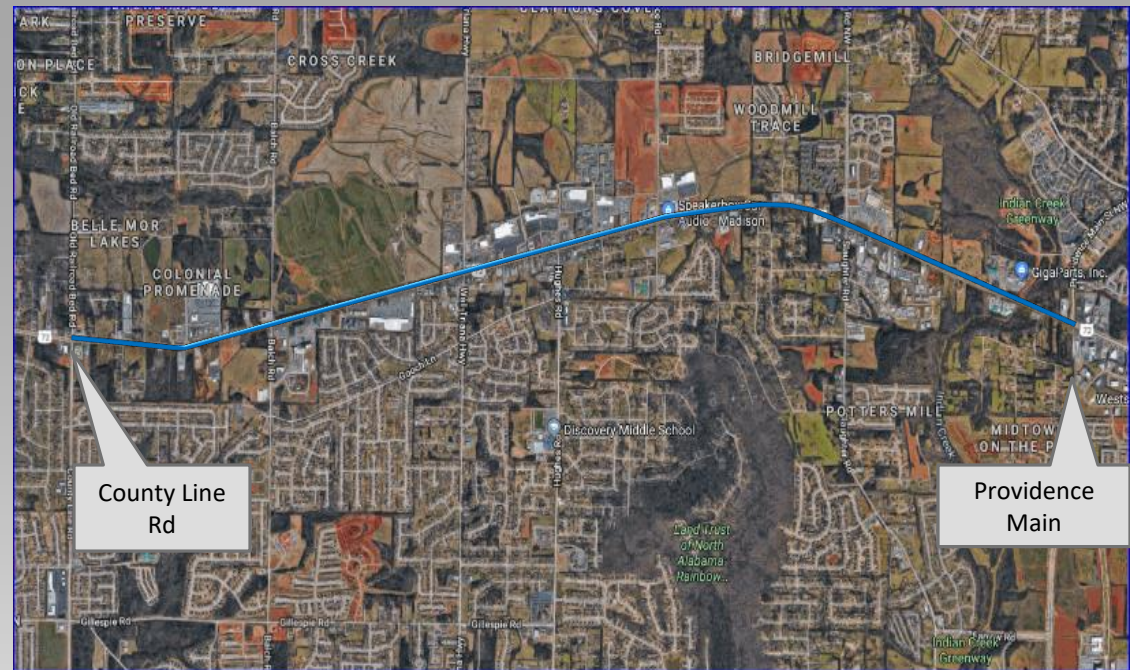

Status: Plans are 30% complete. Multiple funding sources and considering project phases due to budget. Right-of Way acquisition anticipated for FY 2021

Est. Cost \$60,000,000+

Anticipated Start Date: FY 2024

Anticipated Completion Date: FY 2027



# Zierdt Road between Madison Boulevard and Martin Road

Status: Four project phases. Work started in 2015. The last phase (Phase IV) is under contract

Est. Cost (Total) \$27,000,000

Work Started: Fall 2018

25% Complete

Anticipated Completion Date: Mid 2021



# Winchester Road from Naugher Rd to Riverton Rd



Status: Under Construction and about 50% Complete

Cost \$6,597,823

Start Date: February 2019

Anticipated Completion Date: Summer 2020



# Interchange at Blake Bottom Rd and SR 255 (Research Park Blvd)



Status: Substantially complete waiting on Punchlist Inspection

Cost \$7,821,656

Start Date: November 2017

Anticipated Completion Date: May 2020

# Four Bridge Replacements on Old Hwy 431



Status: Project scheduled to begin work 4/20/2020  
Project Awarded to Riley Bridge

Cost \$13,500,000

Estimated Completion FY 2022



# I-565 Interchange Improvements at Greenbrier Rd



Status: Under Construction and 80% complete  
Cost \$10,264,000  
Anticipated Completion Date: Summer 2020

# I-565 Additional Lanes from I-65 to County Line Rd




Status: Project Bids will be received 4/24/2020

Projected Start Date: Work should begin Mid-Summer 2020

Cost \$17,800,000



# Jeff Rd Additional Lanes from South of Capshaw Road to North of Douglas Rd

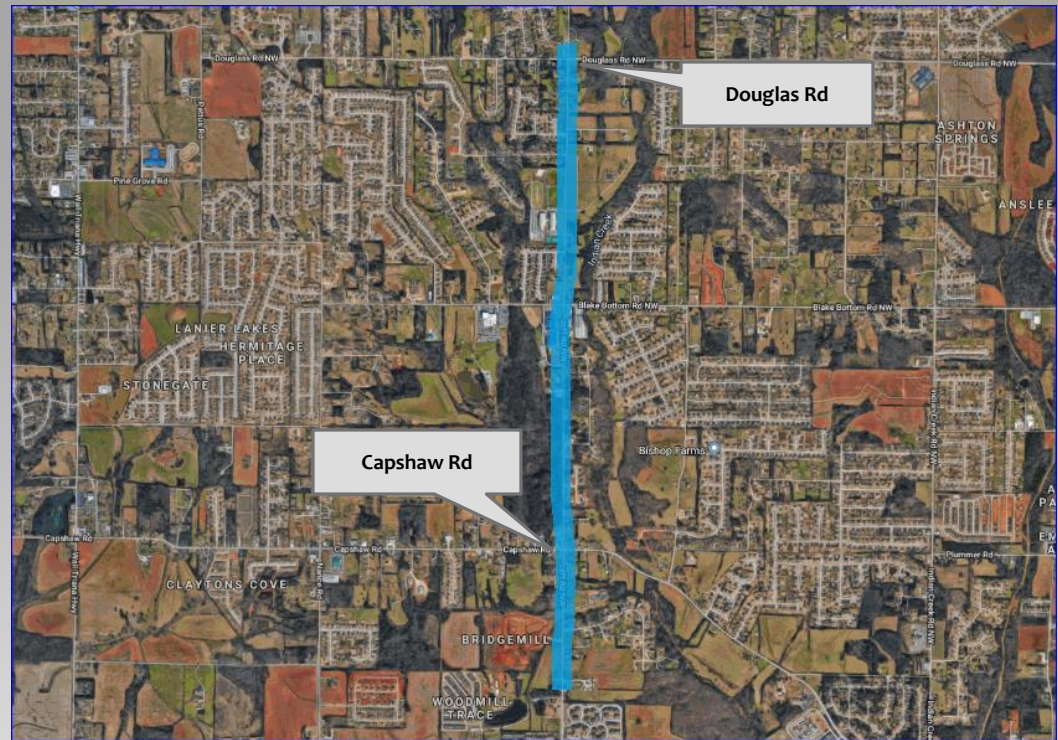

Status: Under Design

Projected Start Date: FY 2021

Cost \$13,500,000

## **Total Amount of Work in Design and Construction**

**\$352,845,277**
