

# Huntsville MPO Project Update

June 17, 2020

# Church Street Phase I between Pratt Avenue and Monroe Street

Status: Under Construction and about  
60% complete

Est. Cost: \$15,627,660

Projected Completion: Winter 2020/2021



# Northern Bypass from Pulaski Pike to US Hwy 231/431



Status: Plans are 85% complete. ROW acquisition to be completed this year.

Est. Cost \$40,000,000

Anticipated Start Date: FY 2021

Anticipated Completion Date: FY 2023



# Martin Road between Zierdt Road and Laracy Drive



Status: Two separate projects that will be built in phases.

Phase I Start Date: July 2018, approximately 35% Complete

Phase I Completion Date: Spring 2021

Phase II is scheduled for FY 2023

Estimated Cost for both phases \$25,000,000

# North Parkway at Mastin Lake Road

Structure Removal Project bids received April 2020. Work Should Begin Summer 2020.

Project Cost: \$520,000

Projected Overpass Project Start Date: FY 2022

## Status

Plans are 90% complete.  
ROW acquisition complete.

Project Cost: \$42,600,000





# Access Management on US 231 between Weatherly Road and Hobbs Road


Status: Plans are 30% complete.  
Anticipate Public Involvement  
Meeting Fall 2020.

Est. Cost \$15,000,000

Anticipated Start Date: Fall 2022  
Anticipated Completion Date:  
Spring 2024



# Cecil Ashburn Drive Improvements

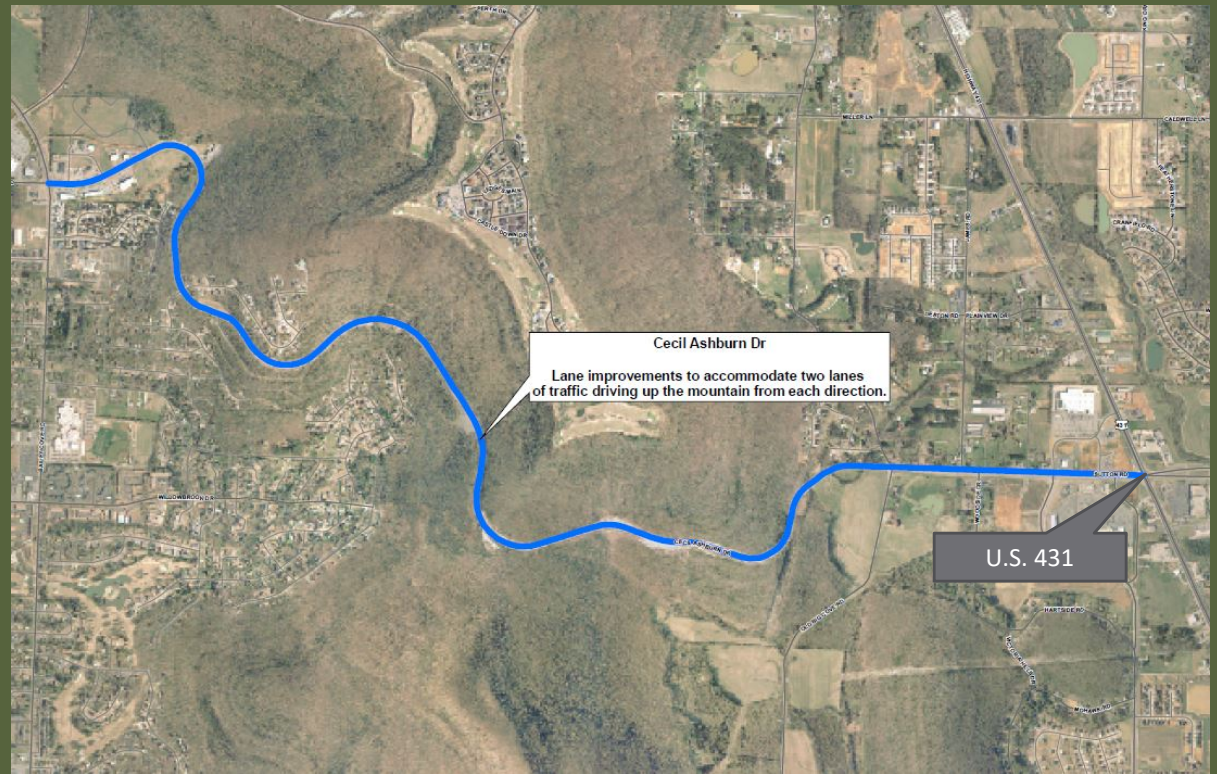


Status: The contractor completed two lanes in October 2019.  
Projected Completion: Late Summer 2020

Est. Cost \$22,000,000



# Winchester Road from Dominion to Naugher Road

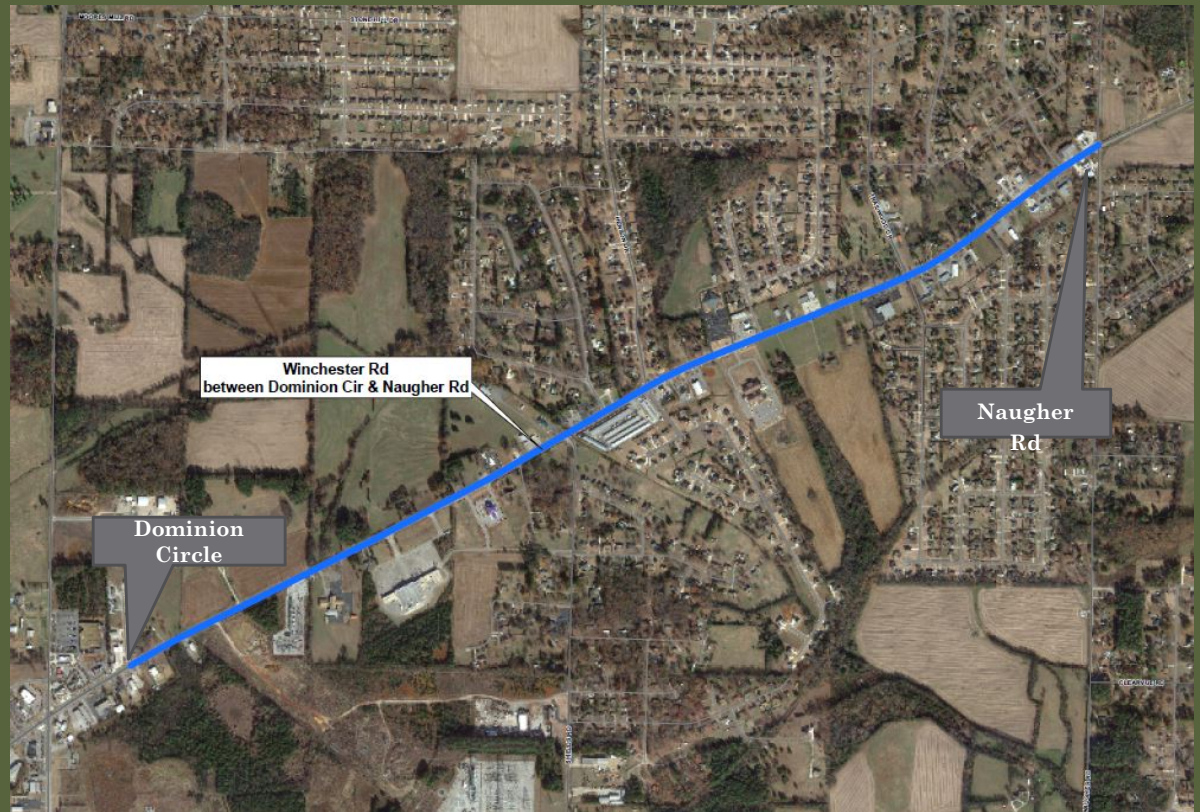

Status: Plans are 90% complete. Right-of Way Acquisition began in 2017

Est. Cost \$15,500,000

Anticipated Start Date: FY 2022

Anticipated Completion Date: FY 2024



# SR 255 (Research Park Boulevard) Widening from US 72 to south of Old Madison Pike

Estimated Cost \$23,415,000

Work started August 2019  
approximately 30% Complete

Anticipated Completion Date:  
Late 2021



# US 72 West between Providence Main and County Line Road



Status: Plans are 30% complete. Multiple funding sources and considering project phases due to budget. Right-of Way acquisition anticipated for FY 2021

Est. Cost \$60,000,000+

Anticipated Start Date: FY 2024

Anticipated Completion Date: FY 2027



# Zierdt Road between Madison Boulevard and Martin Road

Status: Four project phases. Work started in 2015. The last phase (Phase IV) is under contract

Est. Cost (Total): \$27,000,000

Work Started: Fall 2018 35% Complete

Anticipated Completion Date: Mid 2021



# Winchester Road from Naugher Rd to Riverton Rd



Status: Under Construction and about 65% Complete

Cost:\$6,597,823

Start Date: February 2019

Anticipated Completion Date: Fall 2020




# Interchange at Blake Bottom Rd and SR 255 (Research Park Blvd)



Status: Project substantially complete.

Cost \$7,821,656

# Four Bridge Replacements on Old Hwy 431

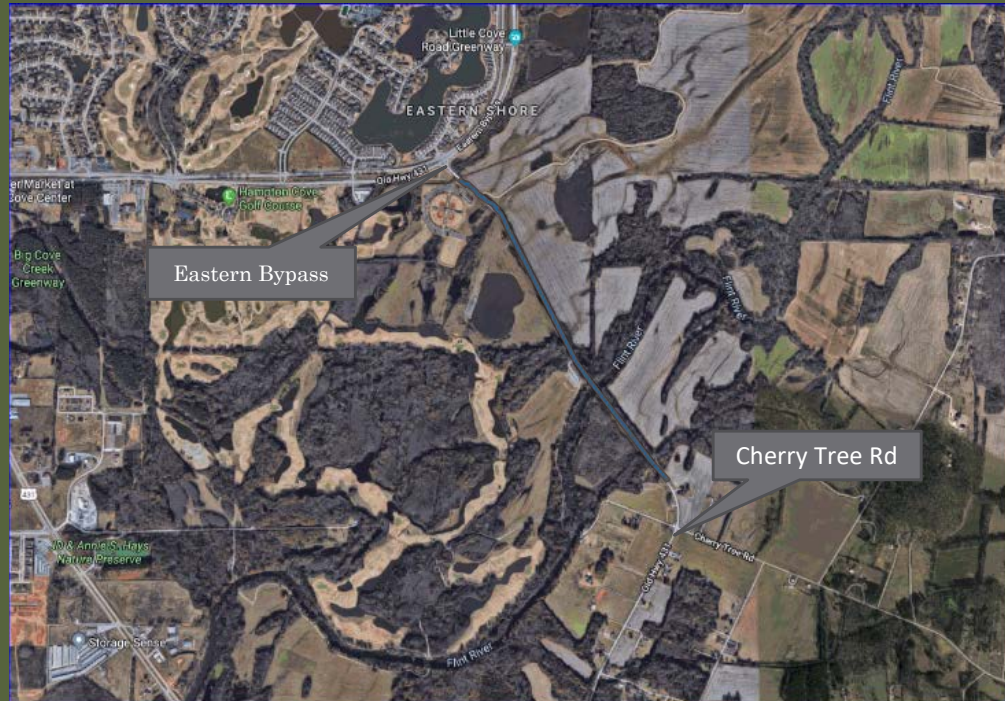

Status: Project under construction and approximately 5% complete.

Cost \$13,500,000

Estimated Completion FY 2022



# I-565 Interchange Improvements at Greenbrier Rd



Status: Under Construction and approximately 85% complete

Cost \$10,264,000

Anticipated Completion Date: Summer 2020

# I-565 Additional Lanes from I-65 to County Line Rd




Status: Bids Received April 2020. Work began this week.

Projected Completion: Fall 2021

Cost \$18,700,000



# Jeff Rd Additional Lanes from South of Capshaw Road to North of Douglas Rd

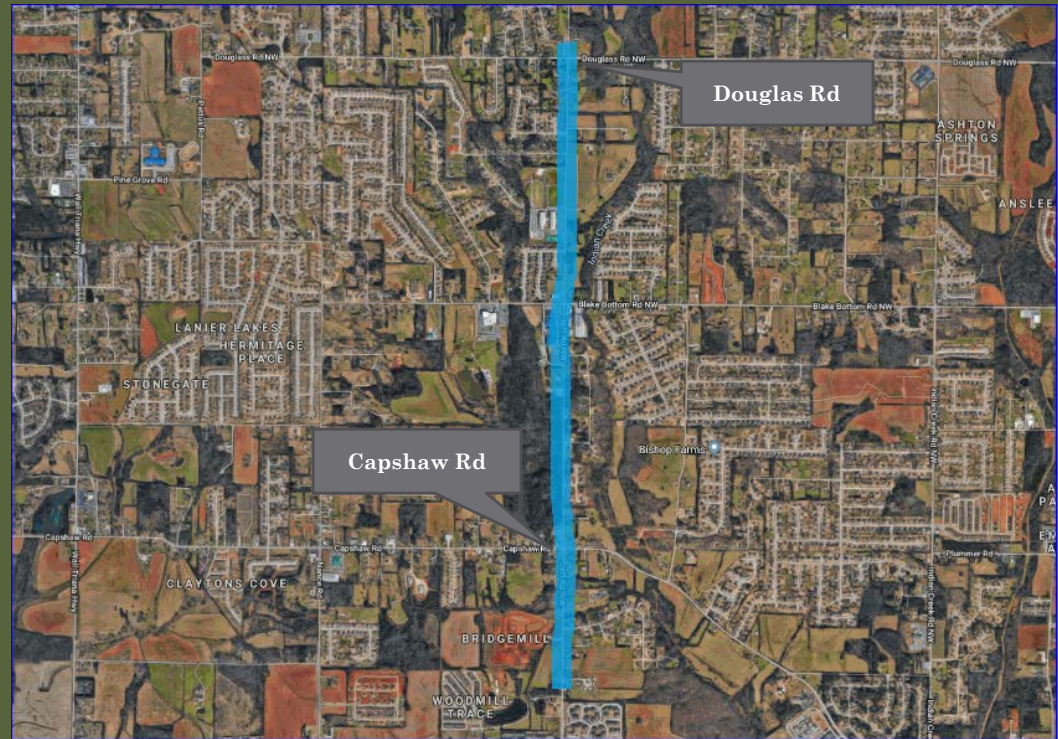

Status: Under Design

Projected Start Date: FY 2021

Cost \$13,500,000

# **Total Amount of Work in Design and Construction**

**\$357,046,139**
