

# Huntsville MPO Project Update

December 2, 2020

# Church Street Phase I between Pratt Avenue and Monroe Street

Status: Under Construction and about  
70% complete

Est. Cost: \$15,627,660

Projected Completion: Summer 2021



# Northern Bypass from Pulaski Pike to US Hwy 231/431



Status: Plans are 85% complete. ROW acquisition to be completed this year.

Est. Cost \$40,000,000

Anticipated Start Date: FY 2021

Anticipated Completion Date: FY 2024



# Martin Road between Zierdt Road and Laracy Drive



Status: Two separate projects that will be built in phases.

Phase I Start Date: July 2018, approximately 50% Complete

Phase I Completion Date: Fall 2021

Phase II is scheduled for FY 2023

Estimated Cost for both phases \$25,000,000

# North Parkway at Mastin Lake Road

Structure Removal Project  
Status: Completed

Project Cost: \$520,000

Projected Overpass Project Start  
Date: FY 2022

## Status

Plans are 90% complete.  
ROW acquisition complete.  
Utility relocation underway.

Project Cost: \$42,600,000






# Access Management on US 231 between Weatherly Road and Hobbs Road


Status: Plans are 50% complete.  
Anticipate Virtual Public  
Involvement Process Spring 2020.

Est. Cost \$15,000,000

Anticipated Start Date: Fall 2022  
Anticipated Completion Date:  
Spring 2024

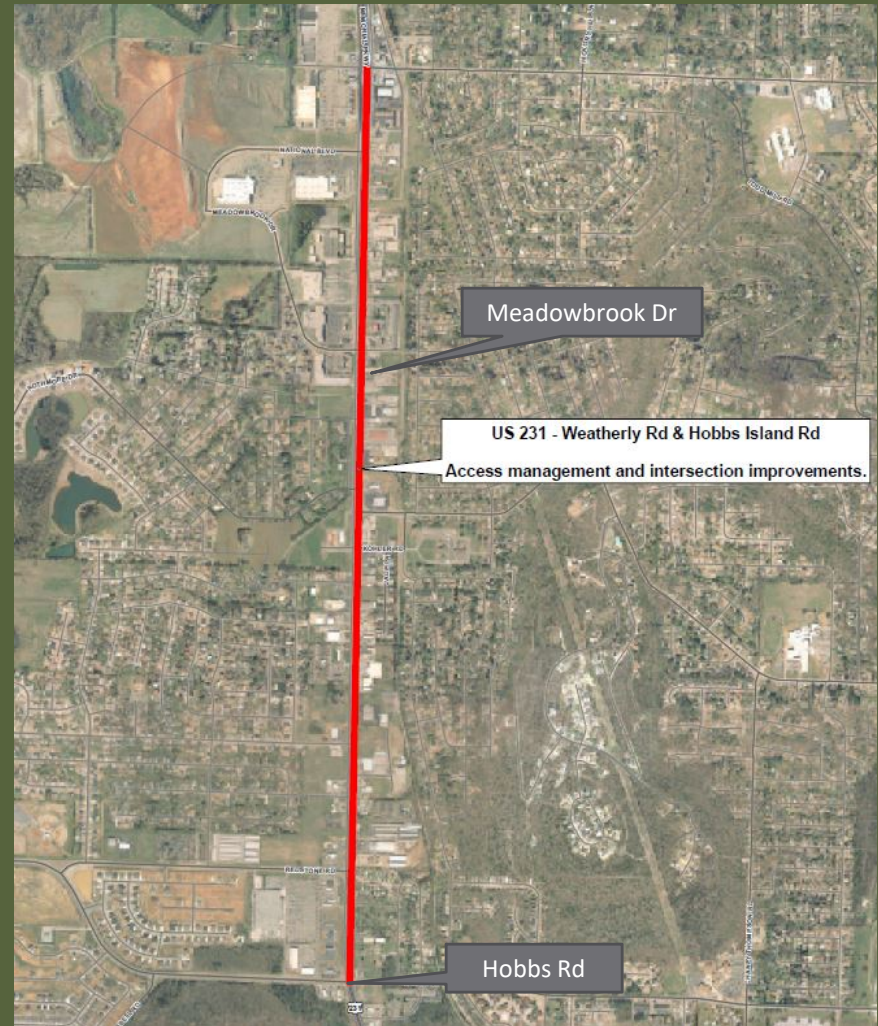

# Winchester Road from Dominion to Naugher Road

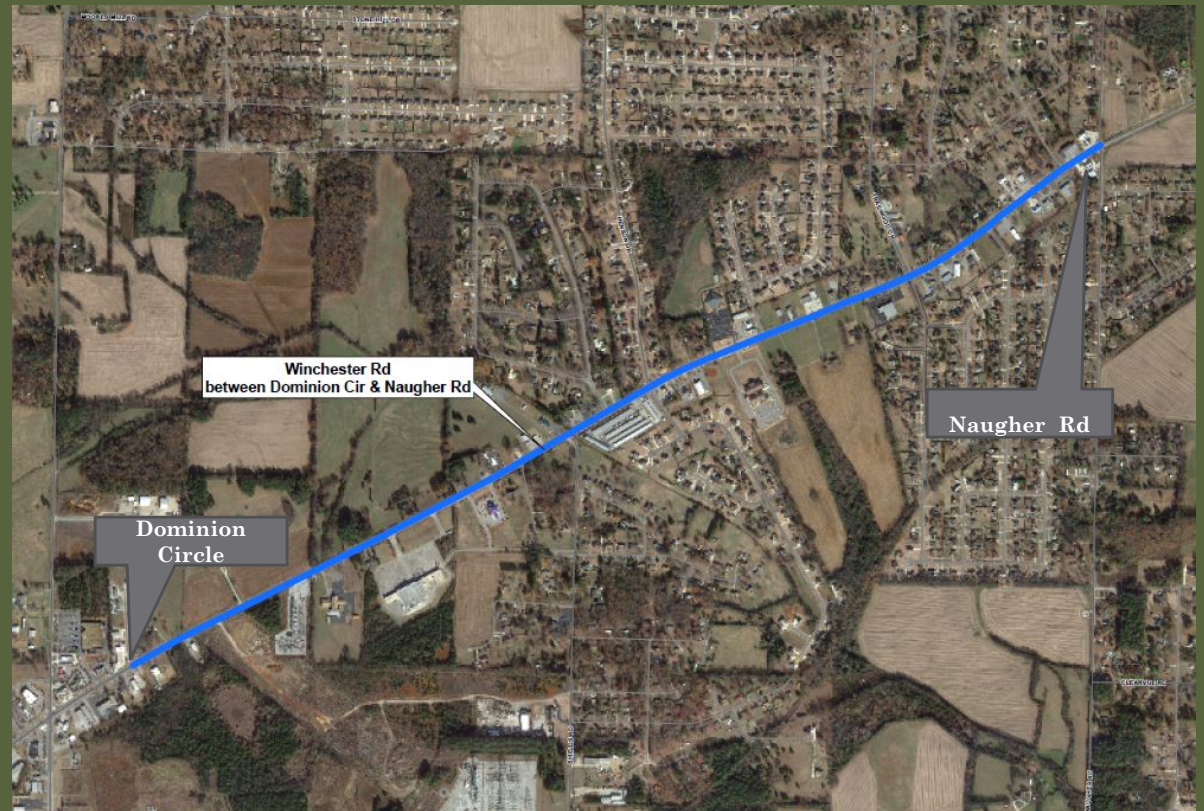

Status: Plans are 90% complete. Right-of Way Acquisition ongoing.

Est. Cost \$15,500,000

Anticipated Start Date: FY 2022

Anticipated Completion Date: FY 2024



# Improvements to Balch Road from South of Browns Ferry Road to North of Gooch Road

Status: Plans are 65% complete.

Est. Cost \$1,700,000

Anticipated Start Date: FY 2022

Anticipated Completion Date: FY 2023





# SR 255 (Research Park Boulevard) Widening from US 72 to south of Old Madison Pike


Estimated Cost \$23,415,000

Work started August 2019  
approximately 60% Complete

Anticipated Completion Date:  
Late 2021



# US 72 West between Providence Main and County Line Road

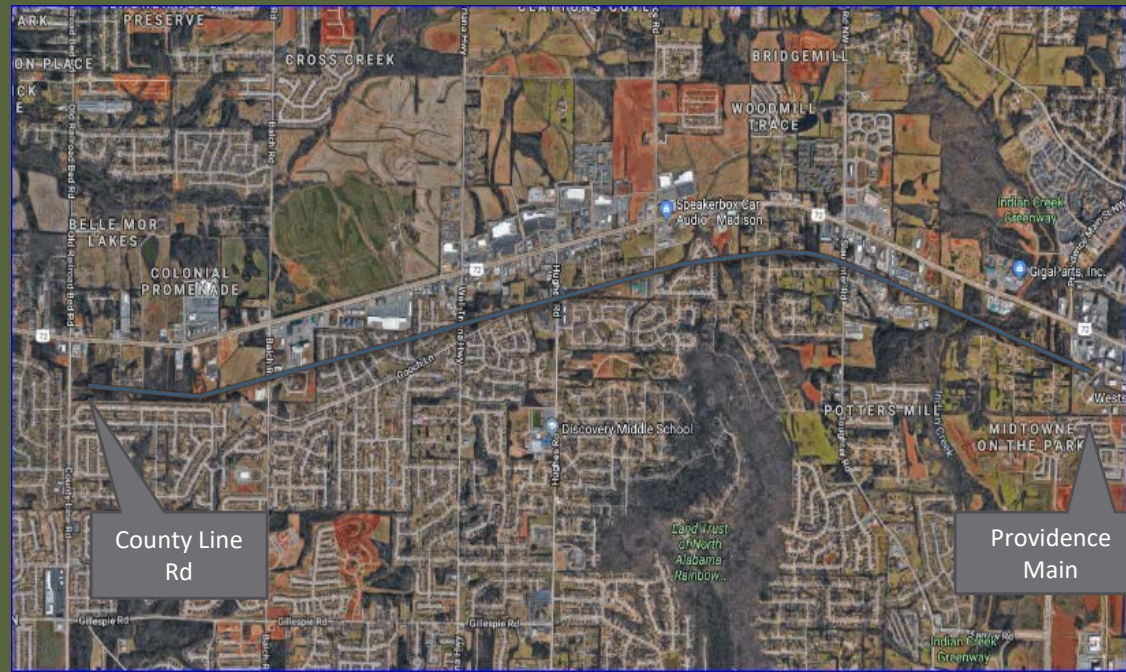

Status: Plans are 30% complete. Multiple funding sources and considering project phases due to budget. Right-of Way acquisition anticipated for FY 2022

Est. Cost \$60,000,000+

Anticipated Start Date: FY 2025

Anticipated Completion Date: FY 2028



# Zierdt Road between Madison Boulevard and Martin Road

Status: Four project phases. Work started in 2015. The last phase (Phase IV) is under contract

Est. Cost (Total): \$27,000,000

Work Started: Fall 2018 Approximately 55% Complete

Anticipated Completion Date: Summer 2021



# Winchester Road from Naugher Rd to Riverton Rd



Status: Under Construction and about 95% Complete


Cost:\$6,597,823

Start Date: February 2019

Anticipated Completion Date: Late 2020



# Four Bridge Replacements on Old Hwy 431

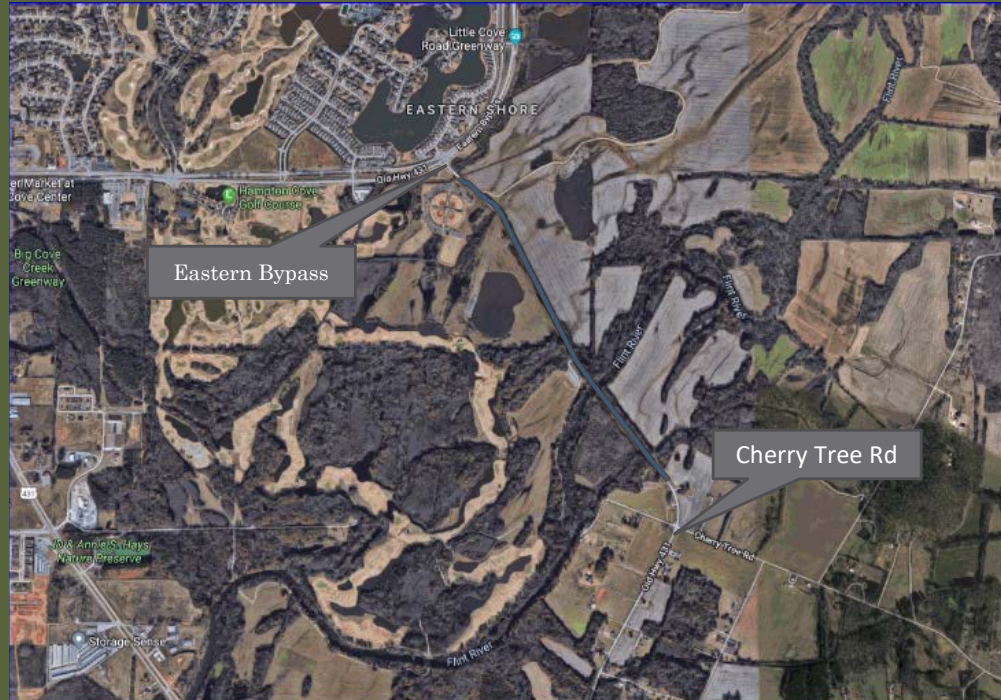

Status: Project under construction and approximately 45% complete.

Cost \$13,500,000

Estimated Completion: Spring 2022

# I-565 Interchange Improvements at Greenbrier Rd



Status: Under Construction and approximately 95% complete

Cost \$10,264,000

Anticipated Completion Date: Late 2020



# I-565 Additional Lanes from I-65 to County Line Rd



Status: Under Construction. Approximately 42% complete.

Projected Completion: Fall 2021

Cost \$18,700,000

# I-565 Additional Lanes from County Line Road to Wall-Triana Highway




Status: Design Phase recently authorized, survey work underway.

Projected Start Date: FY 2024

Cost \$46,800,000



# Jeff Rd Additional Lanes from South of Capshaw Road to North of Douglas Rd

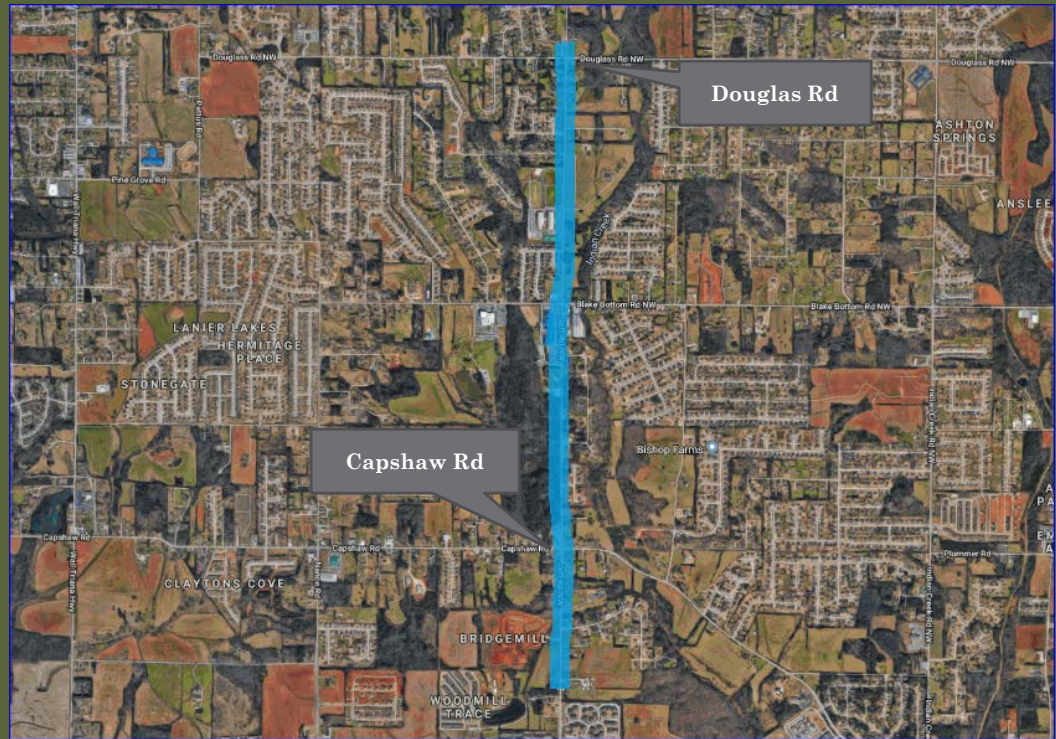

Status: Under Design

Projected Start Date: FY 2022

Cost \$13,500,000

# Intersection Improvements on Wall-Triana Highway at Graphics Drive



Status: Under Design

Projected Start Date: FY 2021

Cost \$1,600,000



# Total Amount of Work in Design and Construction

\$376,804,483
