

# Huntsville MPO Project Update

August 16, 2023

# Northern Bypass from Pulaski Pike to US Hwy 231/431



Status: Plans are complete. ROW acquisition to be completed soon.  
Utility relocation design complete.

Estimated Cost: \$47,000,000

Anticipated Start Date: FY 2023

# Martin Road between Zierdt Road and Laracy Drive



Status: Two separate projects that will be built in phases.

Phase I : Substantially Complete

Phase II is scheduled for FY 2023

Estimated Cost: \$42,000,000 (Both Phases)



# North Parkway at Mastin Lake Road

**Status:** Under construction

**Estimated Cost:** \$45,000,000




# Access Management on US 231 between Weatherly Road and Hobbs Road

Status: Plans are 85% complete.  
ROW acquisition to begin soon.


Estimated Cost: \$15,000,000

Anticipated Start Date: FY 2024

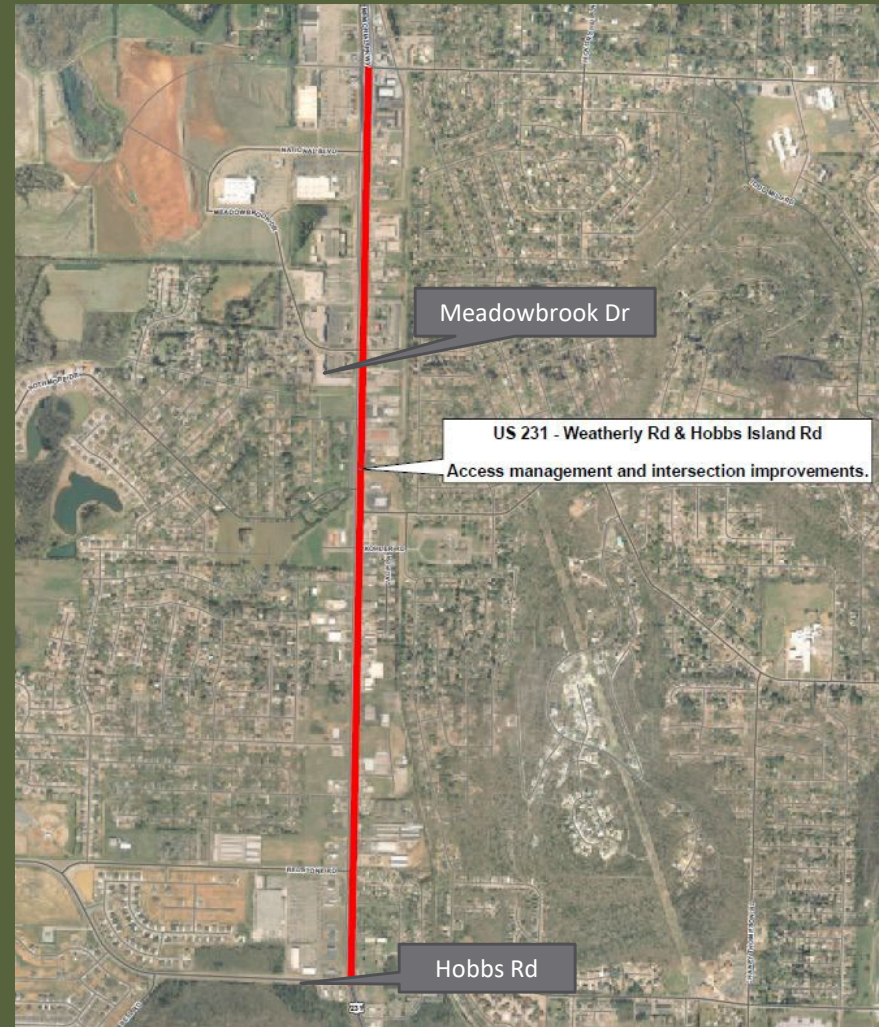



# Winchester Road from Dominion Circle to Naugher Road

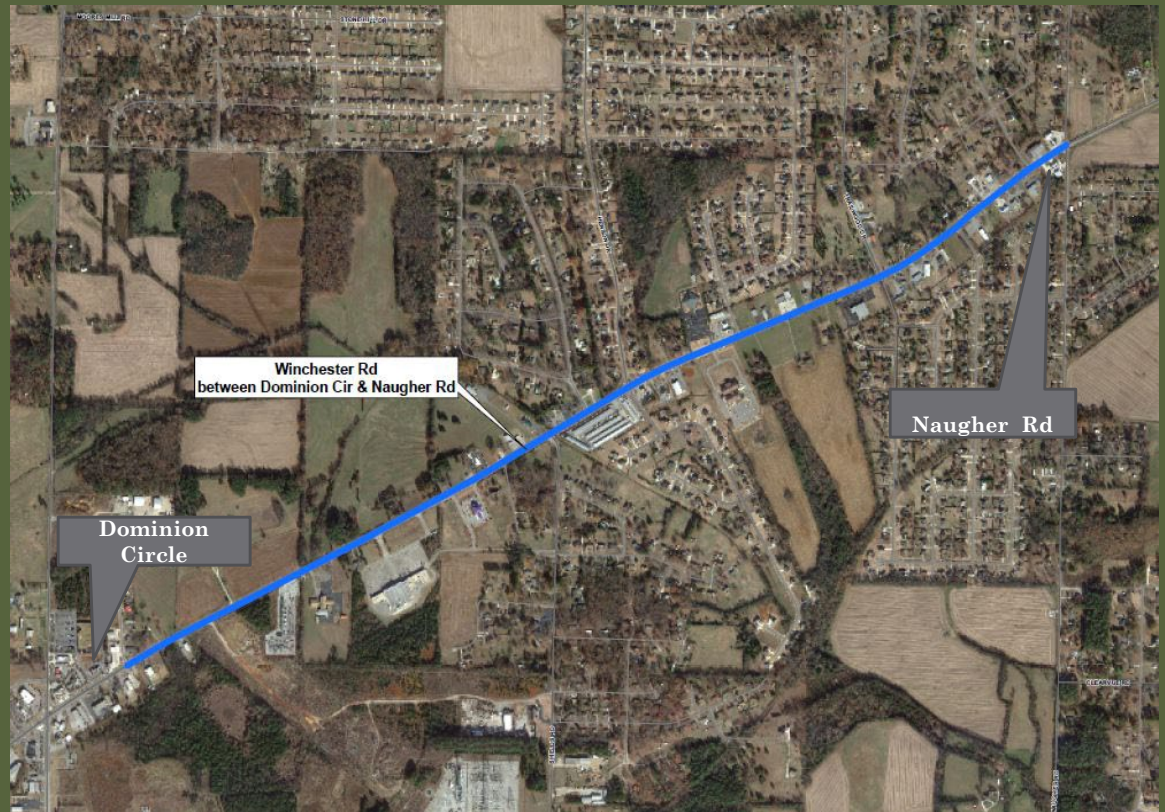

Status: Plans are 90% complete. Right-of Way Acquisition ongoing.  
Utility relocation design work to begin soon.

Estimated Cost: \$28,000,000

Anticipated Start Date: FY 2025

# SR 255 (Research Park Boulevard) Widening from US 72 to south of Old Madison Pike


Status: Substantially Complete

Project Cost \$23,415,000





# US 72 West between Providence Main and County Line Road

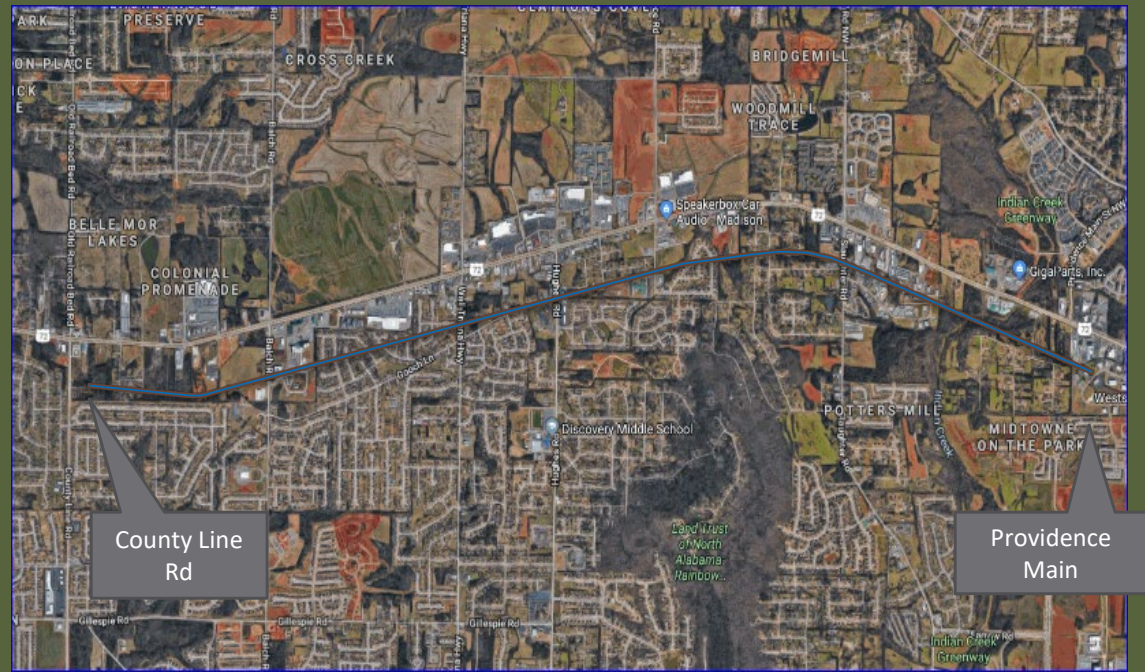

Status: Public Involvement Meeting held May 2022. The project will be broken into multiple phases. Environmental Document will pace schedule.

Phase I: FY 2024 (Plans 90% complete)  
Dates for additional phases not identified at this time.

Estimated Cost: \$85,000,000



# SR-53 Widening from Taurus Drive to Harvest Road

Status: Plans 85% complete

Estimated Cost: \$10,000,000

Anticipated Start Date: FY 2024



# Madison Boulevard from Westchester Road to Flagstone Drive




Status: Plans are 30% complete.

Estimated Cost: \$5,600,000

Anticipated Start Date: FY 2024



# Four Bridge Replacements on Old Hwy 431

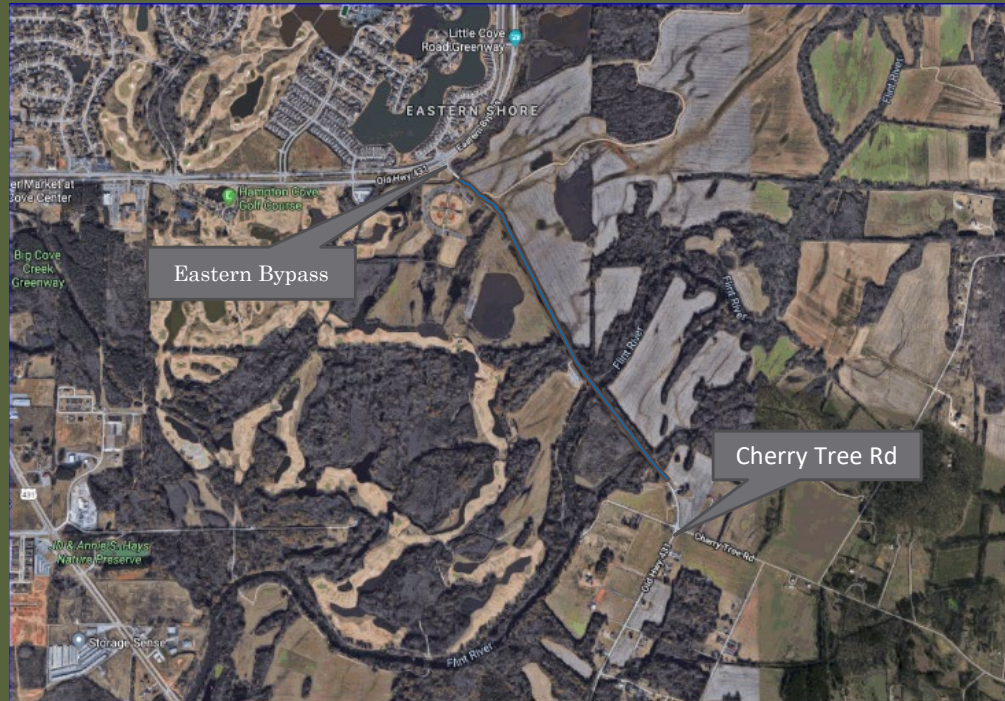

Status: Project substantially complete.

Project Cost: \$13,500,000

# I-565 Additional Lanes from County Line Road to Wall-Triana Highway




Status: Plans 95% complete.

Estimated Cost: \$46,800,000

Anticipated Start Date: FY 2024



# Jeff Rd Additional Lanes from South of Capshaw Road to North of Douglas Rd

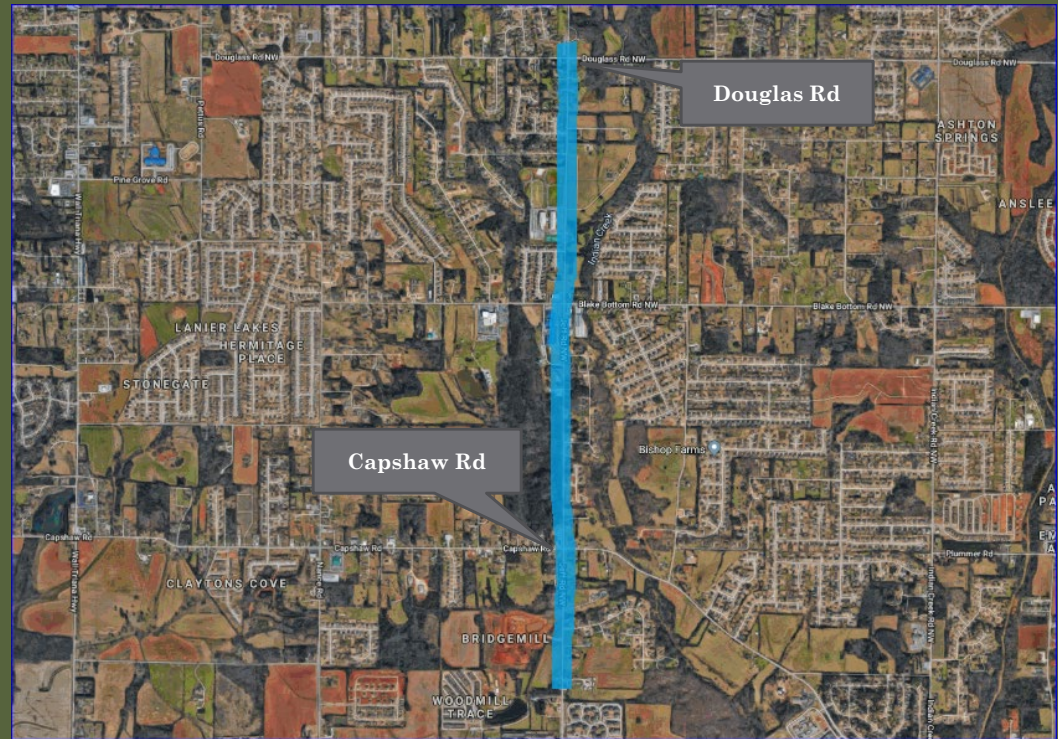

Status: Plans 75% Complete, Virtual Public Involvement concluded April 2021. ROW acquisition anticipated to begin next fiscal year.

Projected Start Date: FY 2025

Estimated Cost: \$13,500,000

# Intersection Improvements on Wall-Triana Highway at Graphics Drive




Status: Approximately 50% complete, work should be completed late fall

Estimated Cost: \$1,879,600



# Widening Blake Bottom Road from Jeff Road to SR 255

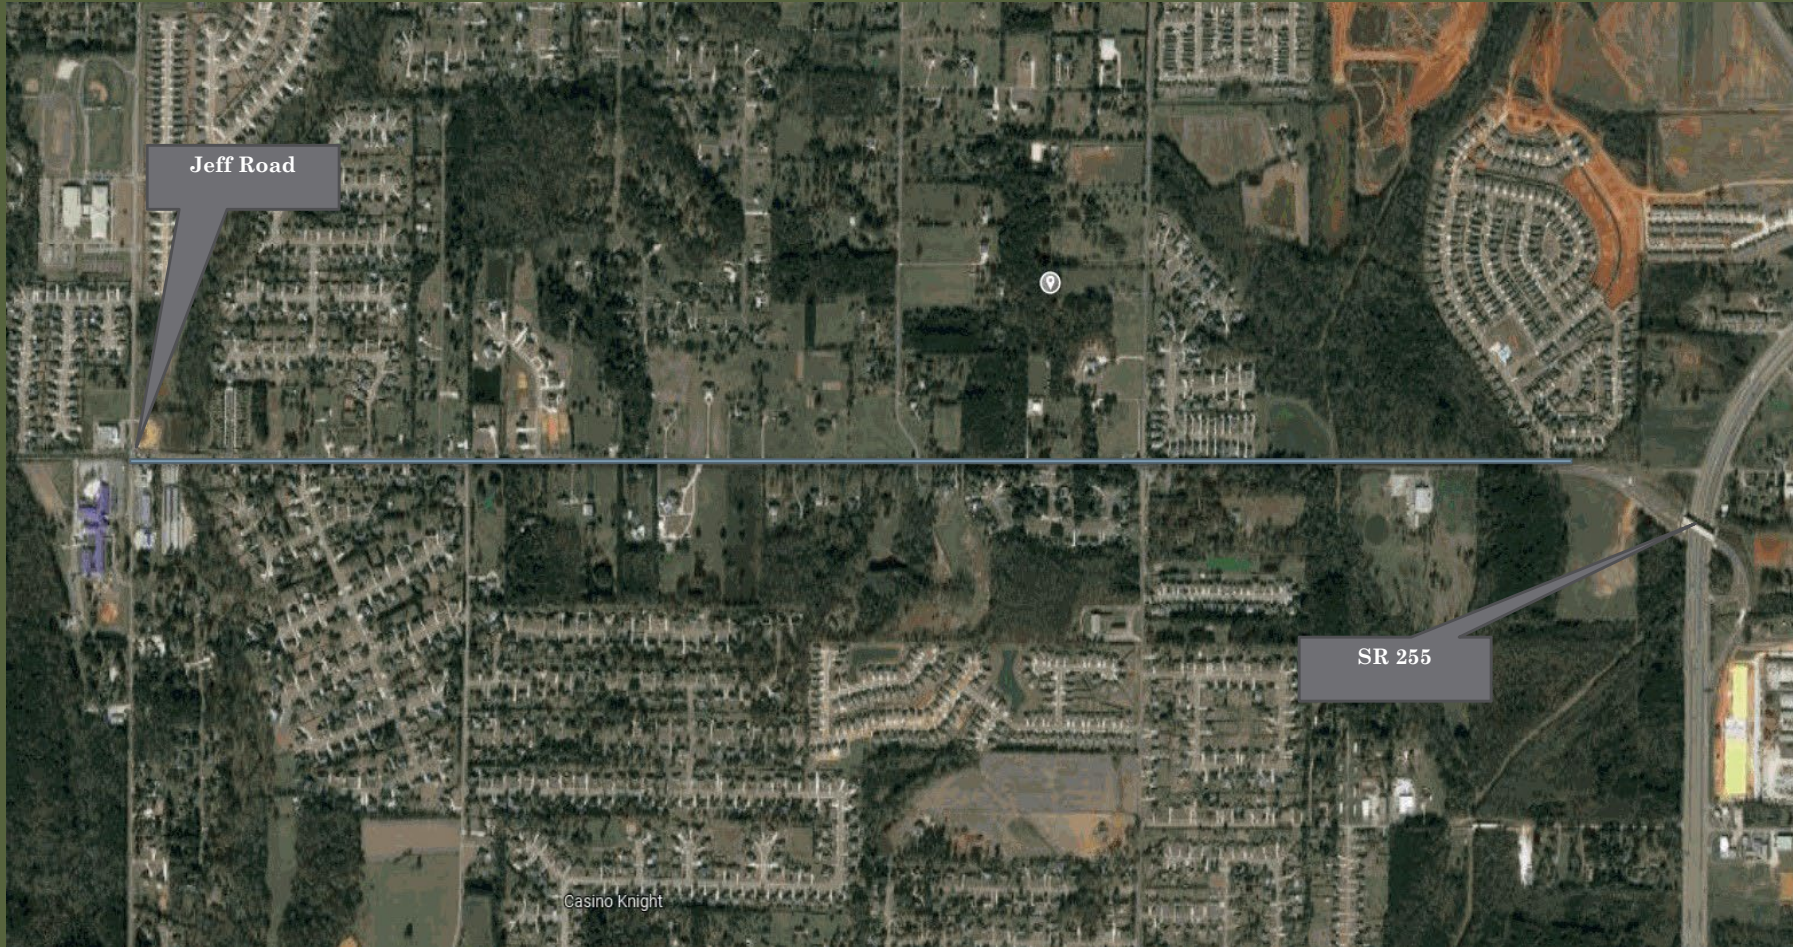

Status: Plans complete. ROW acquisition almost complete.

Estimated Cost: \$20,805,000

Anticipated Start Date: FY 2024



# Intersection Improvements on SR 53 at Harvest, McKee and Old Railroad Bed Roads

Harvest Road



Old Railroad Bed Road



McKee Road

Status: Plans complete.

Estimated Cost: \$5,000,000

Anticipated Start Date: FY 2023

# Arsenal East Connector

Bob Wallace Avenue

Goss Road

Patton Road



Status: Preliminary Engineering underway.

Estimated Cost: \$30,000,000

Anticipated Start Date: FY 2025



**Total Amount of Work in Design and  
Construction**

**\$432,499,600**
