

Huntsville MPO Project Update

March 20, 2024

Northern Bypass from Pulaski Pike to US Hwy 231/431



Status: Utility work is ongoing. Grading work and drainage structure construction is underway.

Project Cost: \$43,000,000

Martin Road between Zierdt Road and Laracy Drive



Status: Two separate projects that will be built in phases.

Phase I : Project Complete

Phase II: Bids received September 29, 2023. Contractor is installing signs.

Project Cost: \$42,000,000 (Both Phases)

North Parkway at Mastin Lake Road

Status: Under construction
Approx. 15% complete.

Project Cost: \$44,200,000




Access Management on US 231 between Weatherly Road and Hobbs Road


Status: Plans are 85% complete.
ROW acquisition to begin soon.

Estimated Cost: \$15,000,000

Anticipated Start Date: FY 2025

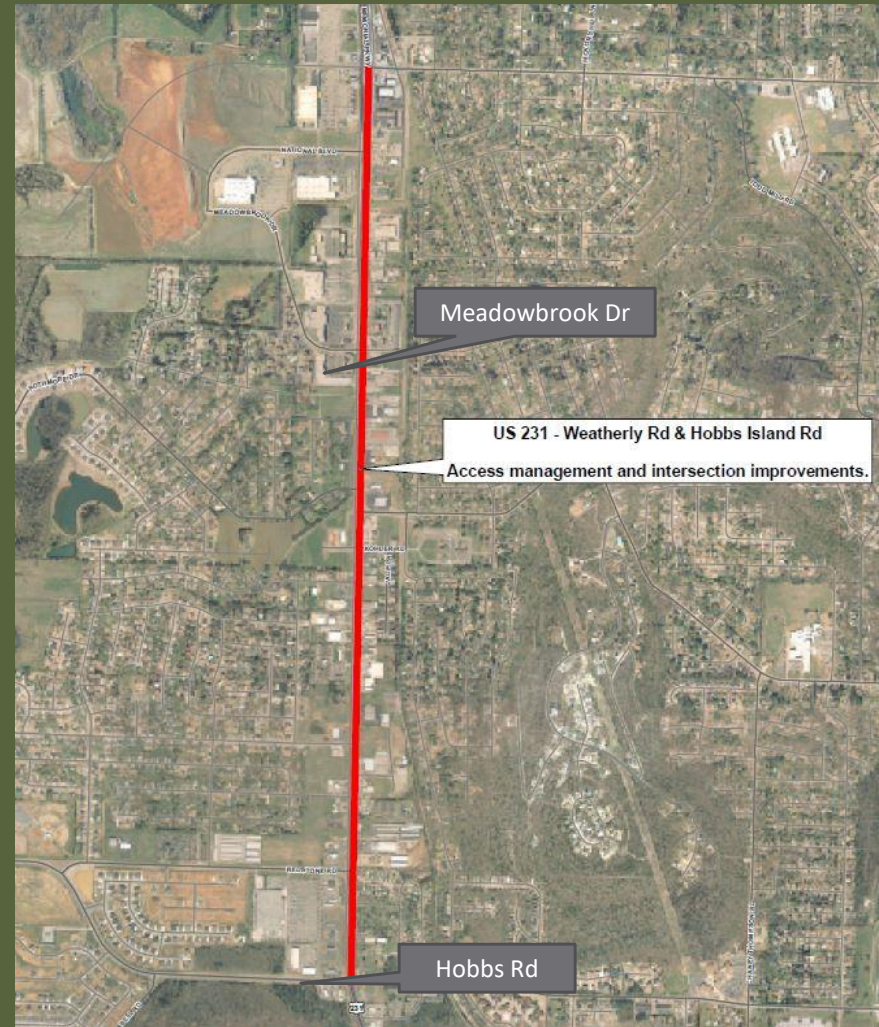

Winchester Road from Dominion Circle to Naugher Road

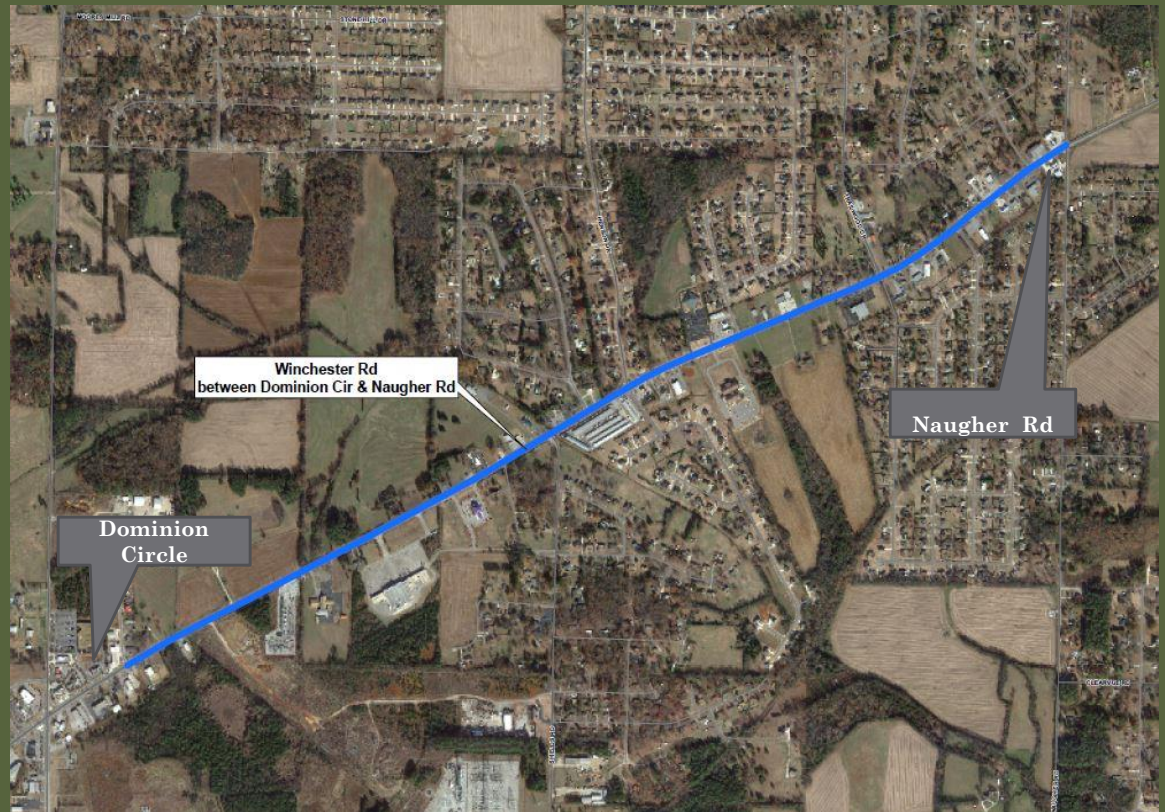

Status: Plans are 90% complete. Right-of Way Acquisition ongoing.
Utility relocation design work to begin soon.

Estimated Cost: \$28,000,000

Anticipated Start Date: FY 2025

SR 255 (Research Park Boulevard) Widening from US 72 to south of Old Madison Pike

Status: Substantially Complete.

Project Cost \$23,415,000



US 72 West between Providence Main and County Line Road



Status: Draft EA (environmental document) to be submitted soon. The project will be broken into multiple phases.

Phase I: FY 2025 (Plans 90% complete)
Dates for additional phases not identified at this time.

Estimated Cost: \$85,000,000

SR-53 Widening from Taurus Drive to Harvest Road

Status: Plans 90% complete

Estimated Cost: \$10,000,000

Anticipated Start Date: FY 2024



Madison Boulevard from Westchester Road to Flagstone Drive




Status: Plans are 90% complete.

Estimated Cost: \$5,600,000

Anticipated Start Date: FY 2024

Four Bridge Replacements on Old Hwy 431

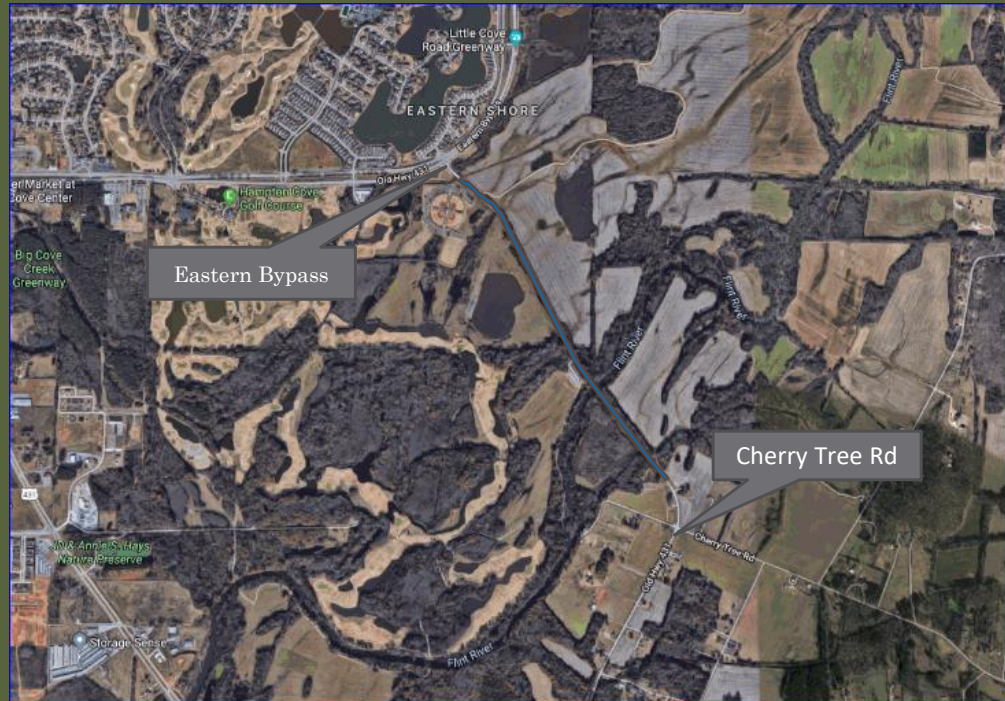

Status: Project substantially complete.

Project Cost: \$13,500,000

I-565 Additional Lanes from County Line Road to Wall-Triana Highway




Status: Plans 95% complete.

Estimated Cost: \$41,400,000

Anticipated Start Date: FY 2024

Jeff Rd Additional Lanes from South of Capshaw Road to North of Douglas Rd

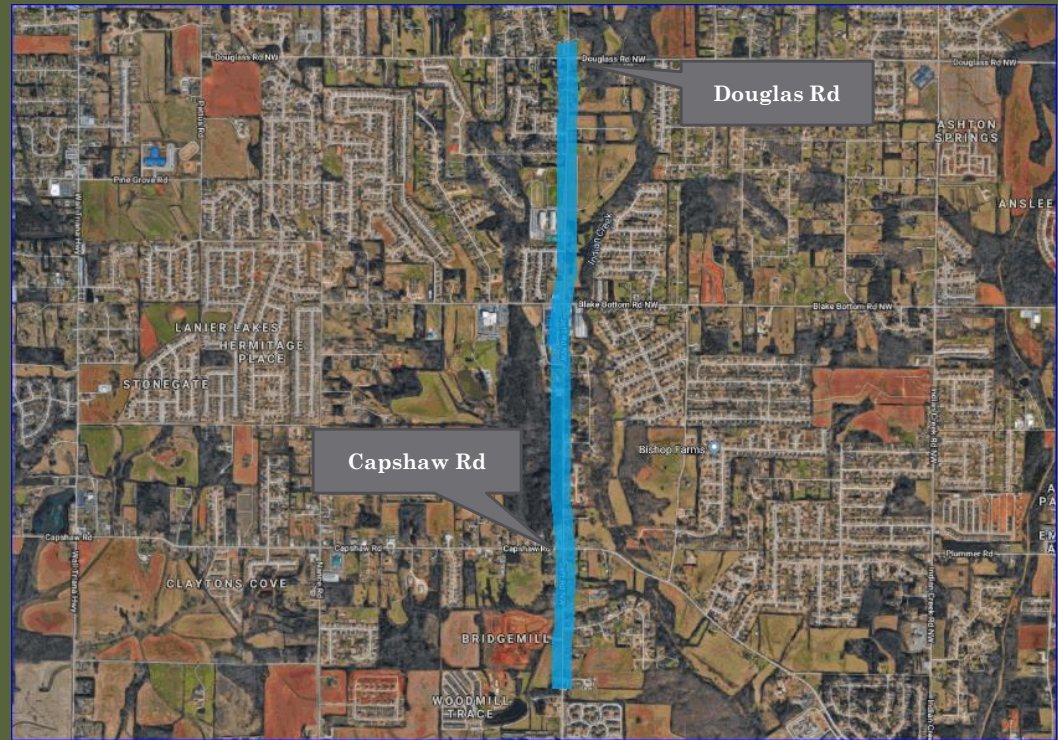

Status: Plans 85% Complete, environmental document submitted for review. ROW acquisition anticipated to begin this fiscal year.

Projected Start Date: FY 2026

Estimated Cost: \$13,500,000


Intersection Improvements on Wall-Triana Highway at Graphics Drive



Status: Accepted for Maintenance.

Estimated Cost: \$1,879,600

Widening Blake Bottom Road from Jeff Road to SR 255

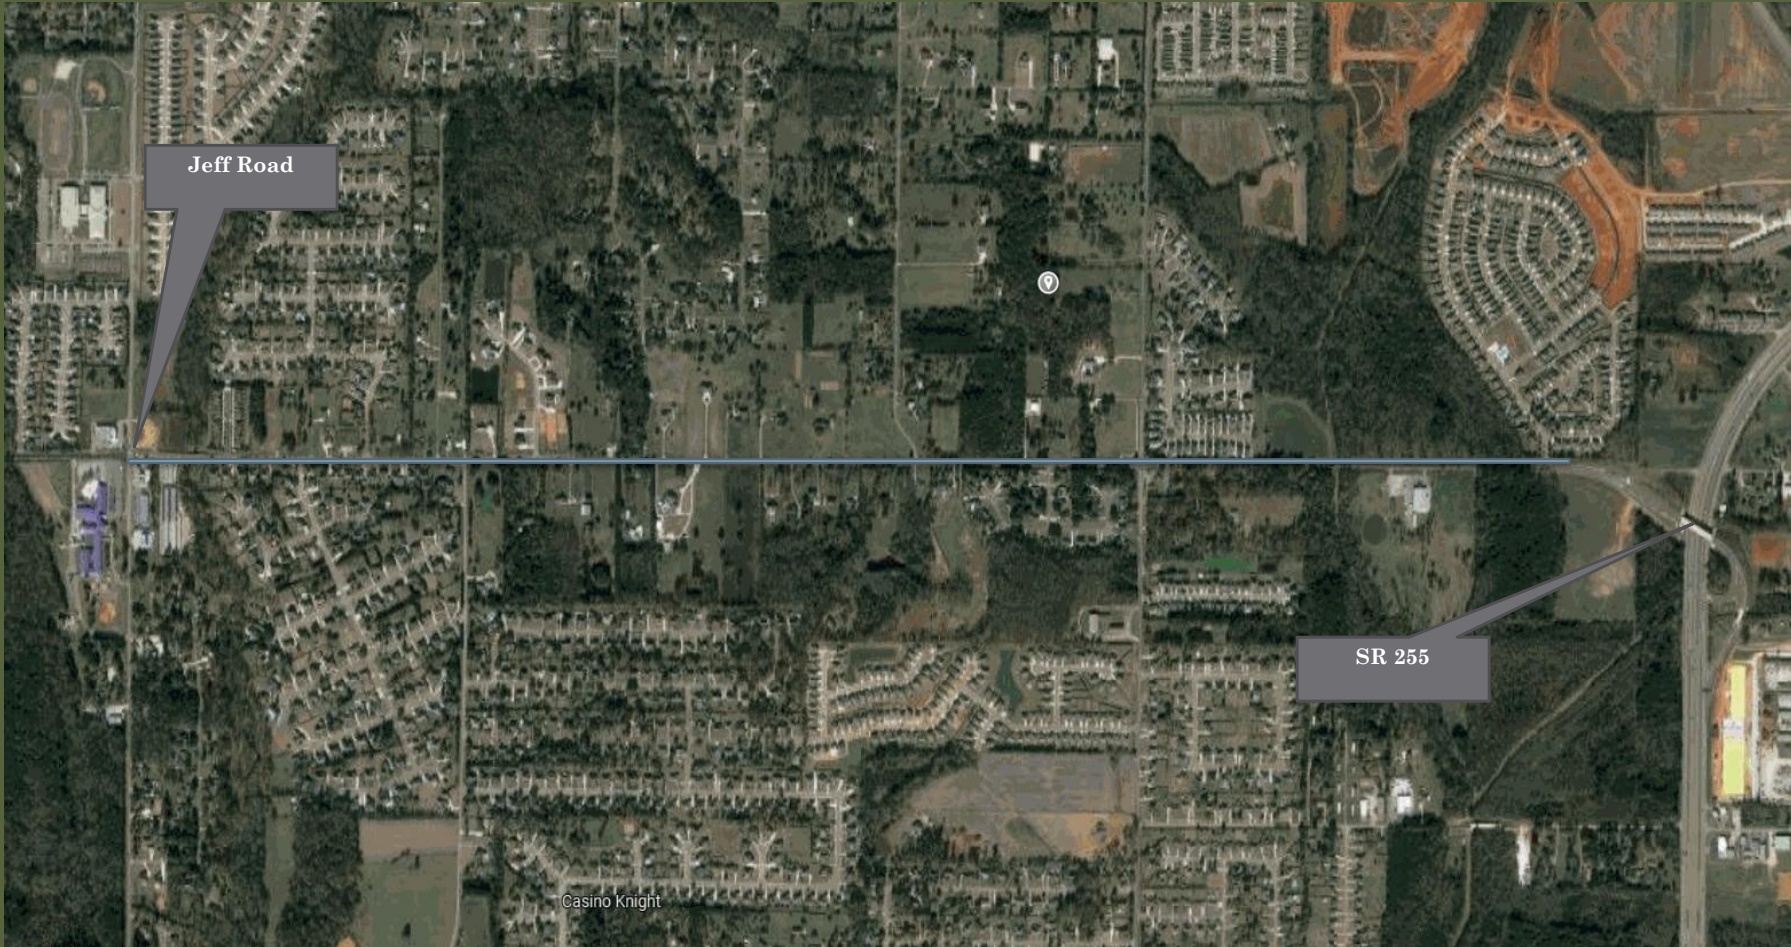

Status: Plans complete. ROW acquisition almost complete. Utility work should begin soon.

Estimated Cost: \$20,805,000

Anticipated Start Date: FY 2025

Intersection Improvements on SR 53 at Harvest, McKee and Old Railroad Bed Roads

Harvest Road



Old Railroad Bed Road



McKee Road

Status: Work anticipated to begin in the next two months.

Project Cost: \$3,700,000

Arsenal East Connector

Bob Wallace Avenue

Goss Road

Patton Road



Status: Preliminary Engineering underway.

Estimated Cost: \$30,000,000

Anticipated Start Date: FY 2028

**Total Amount of Work in Design and
Construction**

\$420,999,600
