

Huntsville MPO Project Update

August 7, 2024

Northern Bypass from Pulaski Pike to US Hwy 231/431



Status: Utility work is ongoing. Grading work and drainage structure construction is underway. Project approximately 10% complete.

Project Cost: \$43,000,000

Martin Road between Zierdt Road and Laracy Drive



Status: Two separate projects that will be built in phases.

Phase I : Project Complete

Phase II: Utility relocation is underway. Grading and drainage work to begin soon. Project approximately 5% complete.

Project Cost: \$42,000,000 (Both Phases)


North Parkway at Mastin Lake Road

Status: Under construction
Approx. 20% complete.

Project Cost: \$44,200,000



Winchester Road from Dominion Circle to Naugher Road

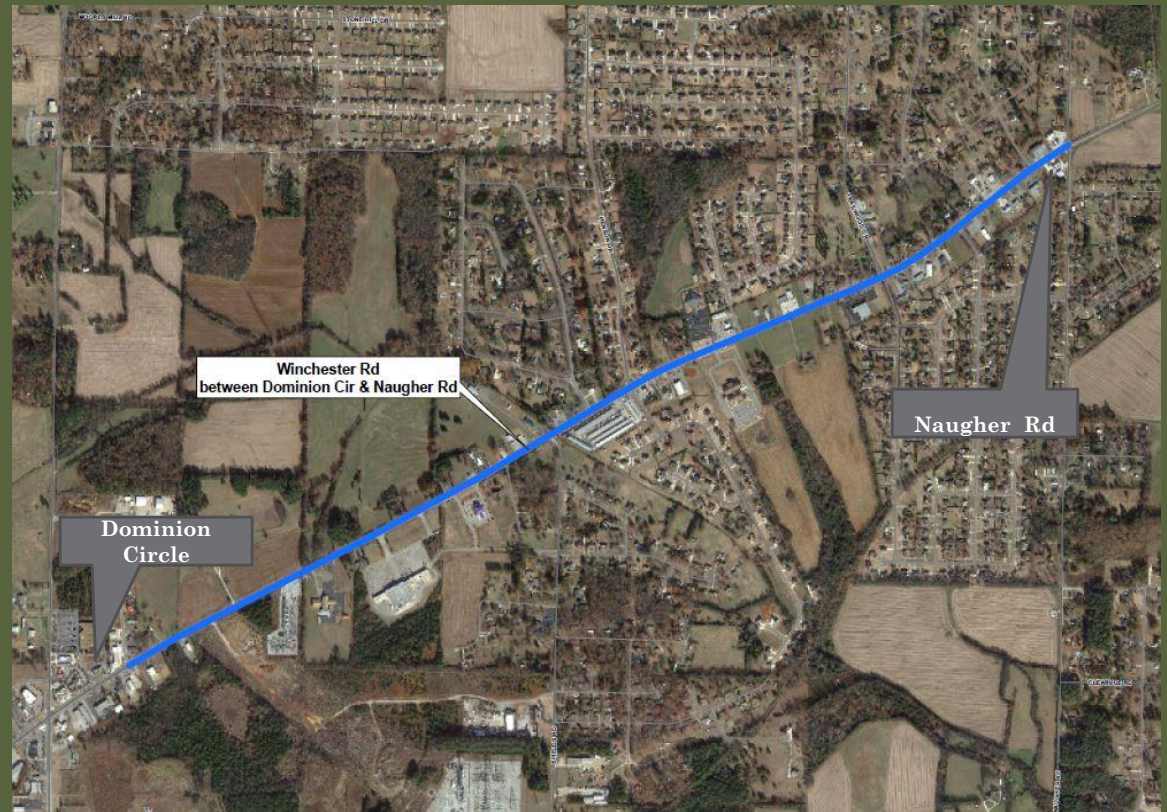

Status: Plans are 90% complete. Right-of Way Acquisition ongoing.
Utility relocation design work to begin soon.

Estimated Cost: \$28,000,000

Anticipated Start Date: FY 2026

US 72 West between Providence Main and County Line Road



Phase I – Huntsville Memorial Gardens to Providence Main

Status: Draft EA (environmental document) to be submitted soon.

Phase I: FY 2025 (Plans 90% complete)

Estimated Cost: \$18,000,000

US 72 West between Providence Main and County Line Road



Phase II – Walnut Street to Huntsville Memorial Gardens

Status: Preliminary Engineering scheduled to start Fall 2024, CN planned for FY 2027

Estimated Cost: \$36,000,000

US 72 West between Providence Main and County Line Road



Phase III – County Line Road to Walnut Street

Status: Preliminary Engineering scheduled to start FY 25, CN planned for FY 2030

Estimated Cost: \$33,000,000

SR-53 Widening from Taurus Drive to Harvest Road

Status: Plans 90% complete

Estimated Cost: \$10,000,000

Anticipated Start Date: FY 2025




Madison Boulevard from Westchester Road to Flagstone Drive



Status: Bids received June 2024. Work should begin soon.

Estimated Cost: \$4,200,000

Four Bridge Replacements on Old Hwy 431

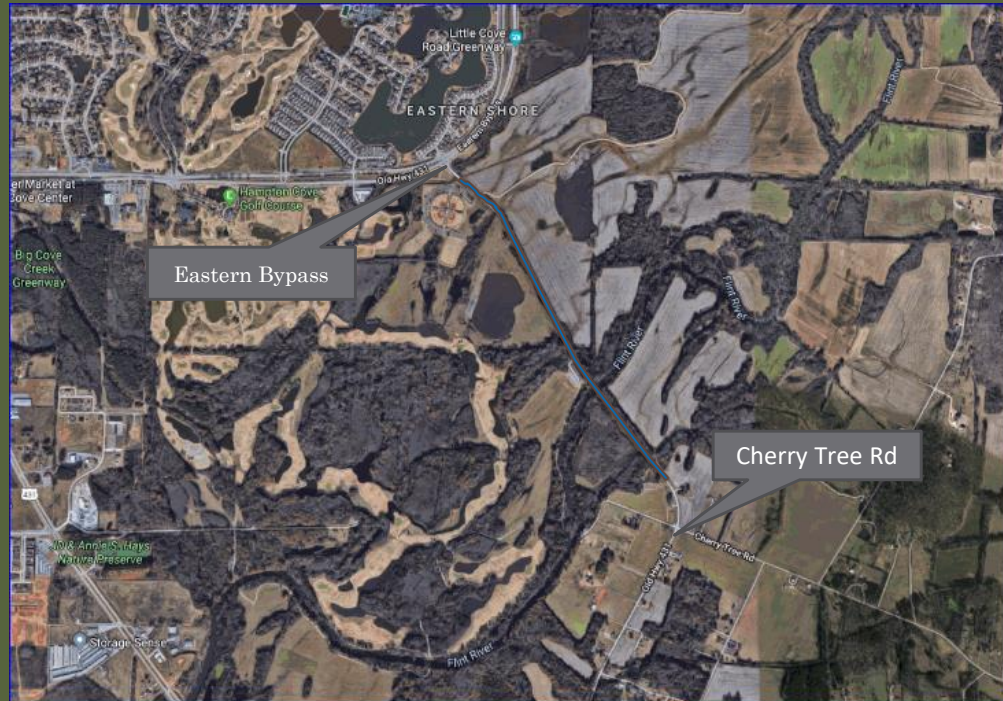

Status: Project complete.

Project Cost: \$13,500,000


I-565 Additional Lanes from County Line Road to Wall-Triana Highway



Status: Bids received May 2024. Contractor should begin work soon.

Estimated Cost: \$41,800,000

Jeff Rd Additional Lanes from South of Capshaw Road to North of Douglas Rd

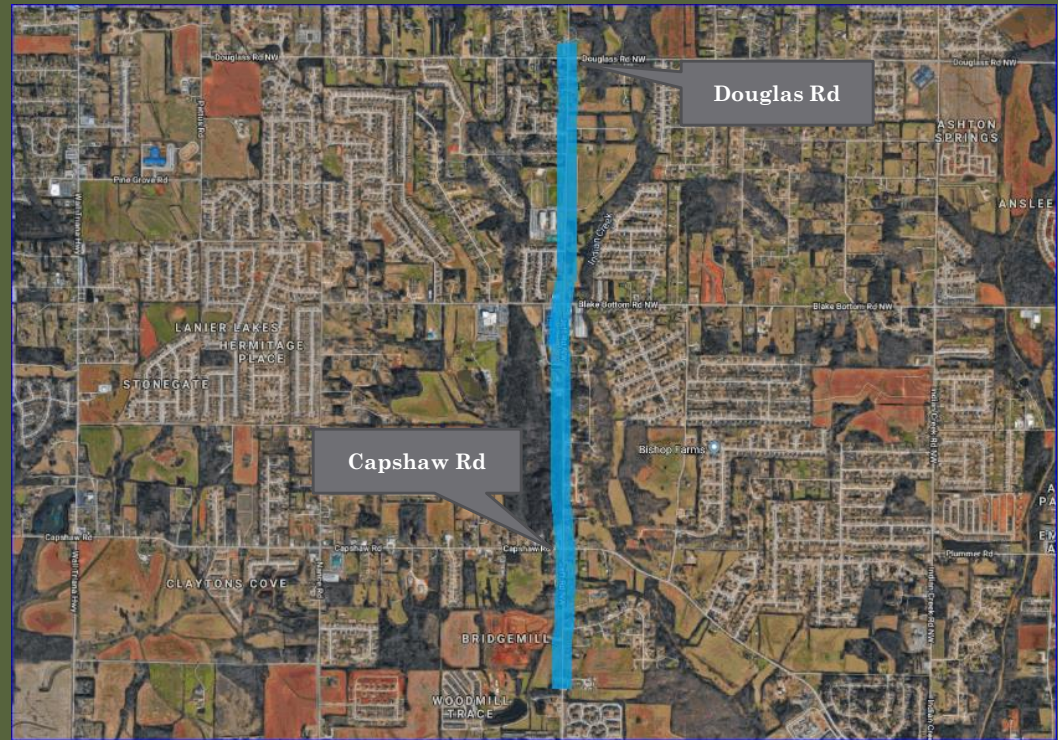


Status: Plans 85% complete, environmental document submitted for review. ROW acquisition anticipated to begin next fiscal year.

Projected Start Date: FY 2026

Estimated Cost: \$13,500,000

Widening Blake Bottom Road from Jeff Road to SR 255

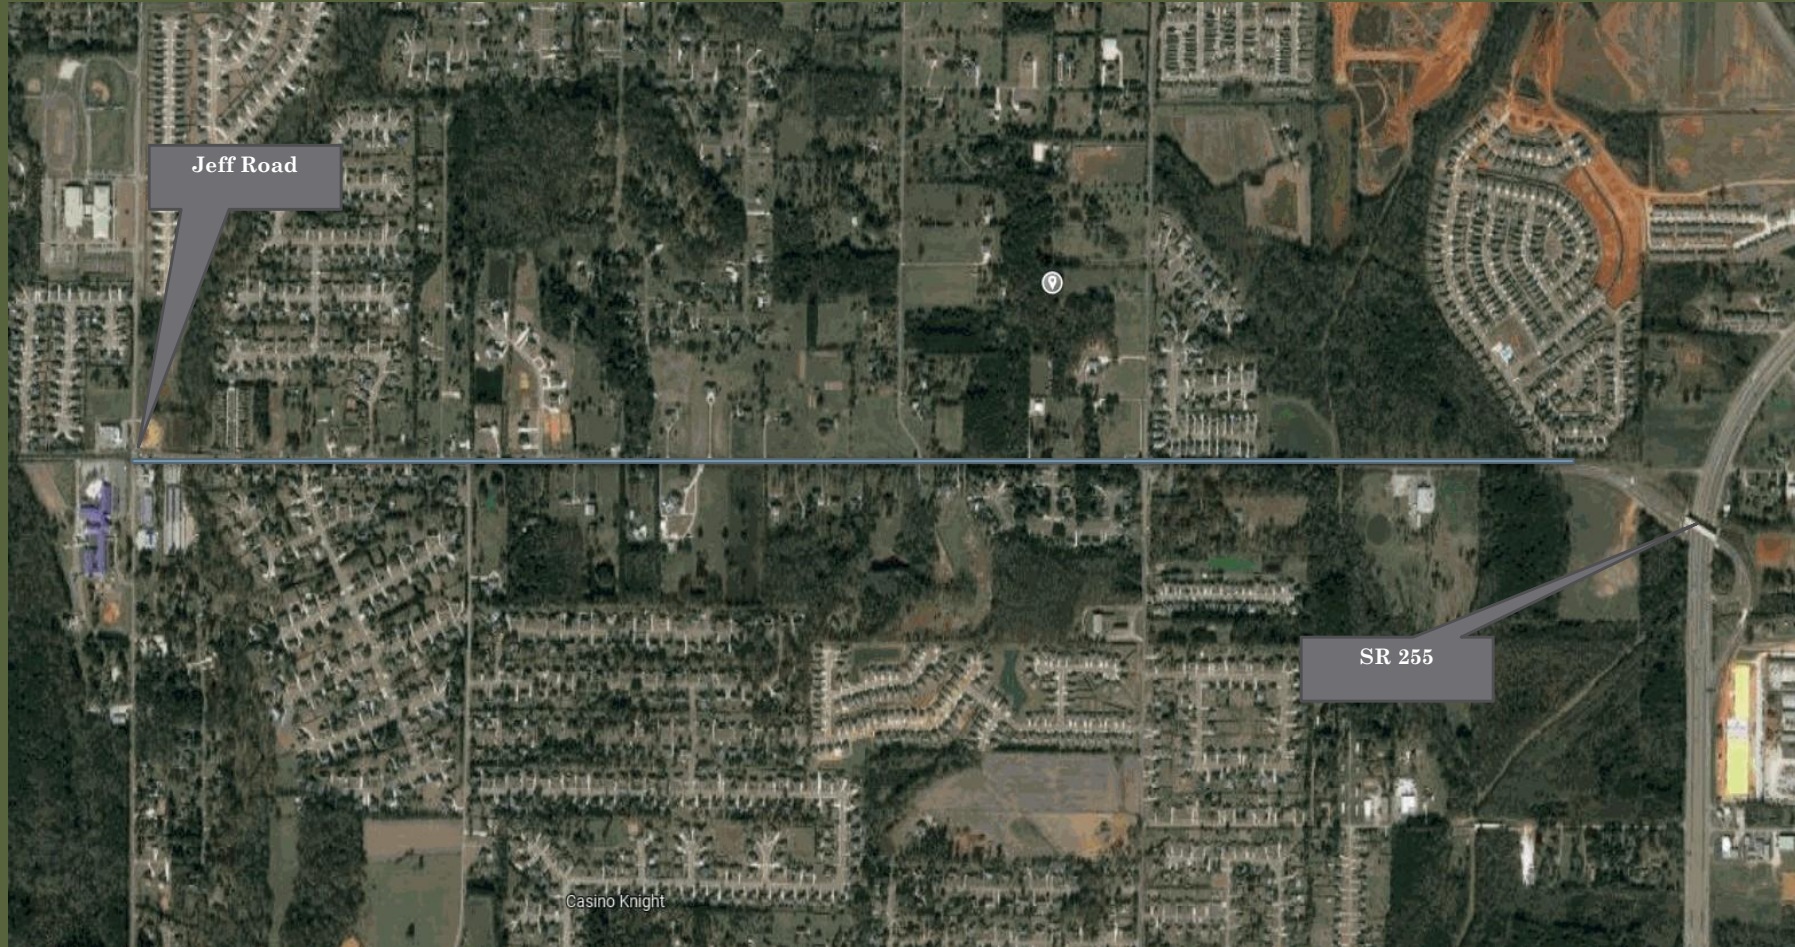

Status: Plans and ROW acquisition complete. Clearing for utilities is underway. Utility work should begin soon. Construction project to be bid by County in Fiscal Year 2025.

Estimated Cost: \$20,805,000

Anticipated Start Date: FY 2025

Intersection Improvements on SR 53 at Harvest, McKee and Old Railroad Bed Roads

Harvest Road



Old Railroad Bed Road




McKee Road

Status: Work underway, approximately 15% complete.

Project Cost: \$3,700,000

Arsenal East Connector

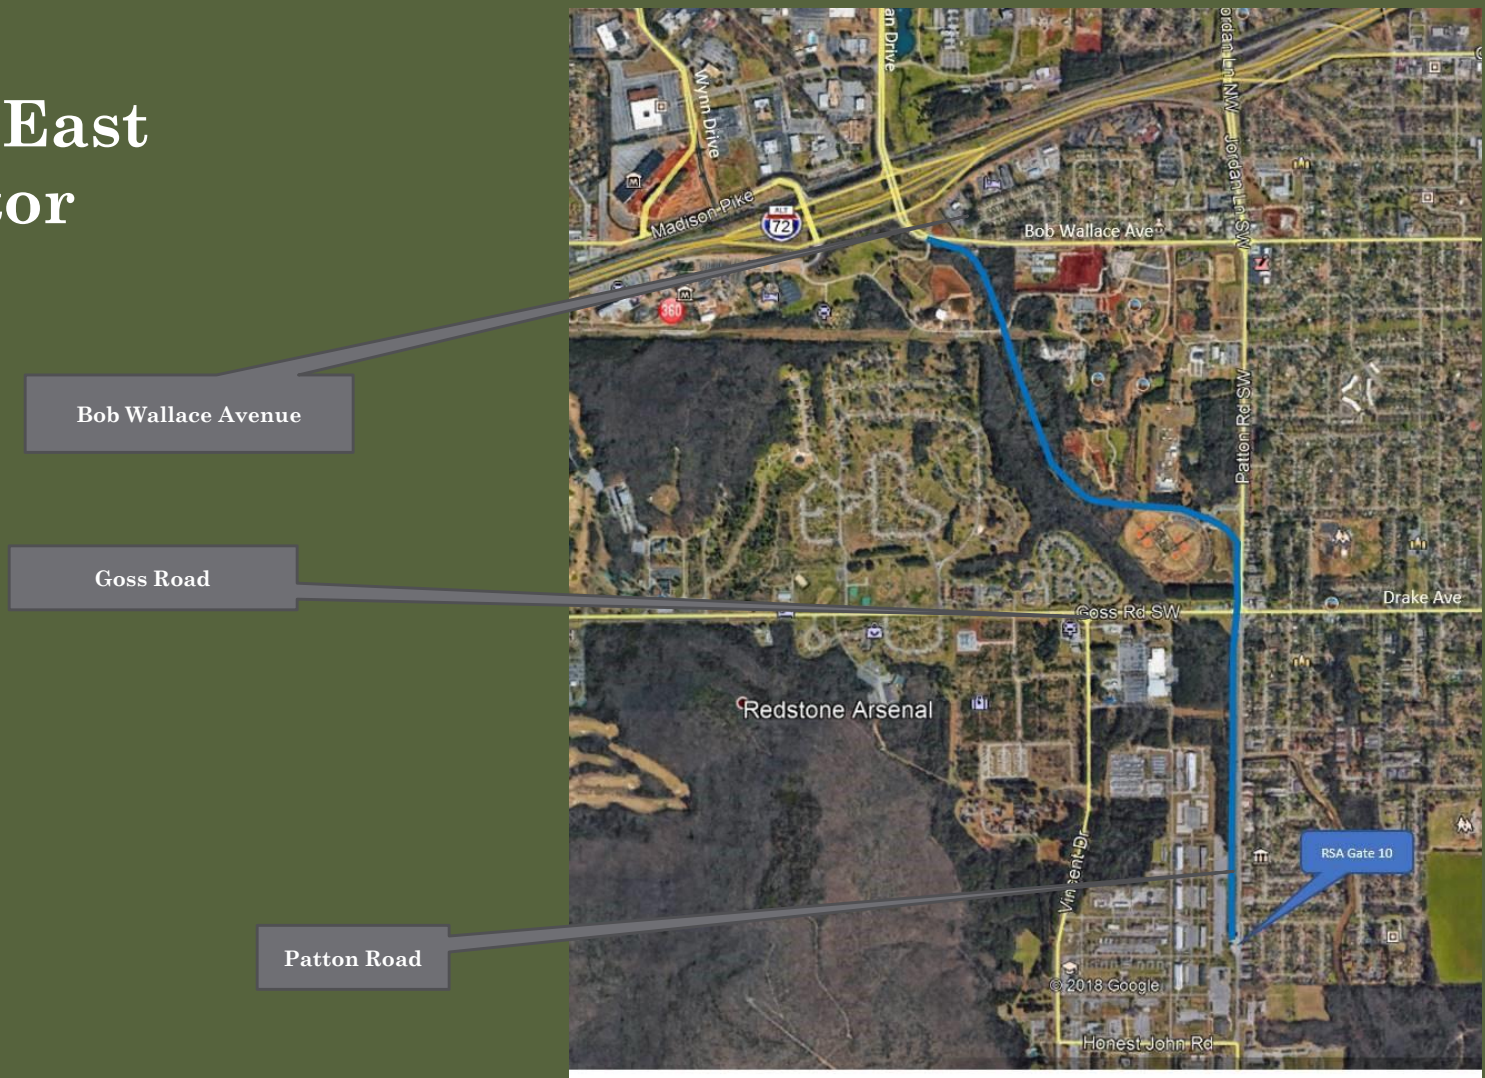

Status: Preliminary Engineering underway.

Estimated Cost: \$30,000,000

Anticipated Start Date: FY 2028

**Total Amount of Work in Design and
Construction**

\$396,705,000
