

# Huntsville MPO Project Update

May 21, 2025

# Northern Bypass from Pulaski Pike to US Hwy 231/431



Status: Utility work is ongoing. Grading work and drainage structure construction is underway. Project approximately 40% complete.

Project Cost: \$43,000,000

# Martin Road between Zierdt Road and Laracy Drive



Status: Two separate projects that will be built in phases.

Phase I : Project Complete

Phase II: Utility relocation is underway. Bridge foundation construction is underway. Grading and drainage work is underway east of Bradford Creek. Project approximately 25% complete.

Project Cost: \$42,000,000 (Both Phases)



# North Parkway at Mastin Lake Road

**Status:** Under construction  
Approx. 45% complete.

Project Cost: \$44,200,000




# Access Management on US 231 between Weatherly Road and Hobbs Road

Status: Plans are 85% complete.  
ROW acquisition to begin soon.


Estimated Cost: \$15,000,000

Anticipated Start Date: FY 2026

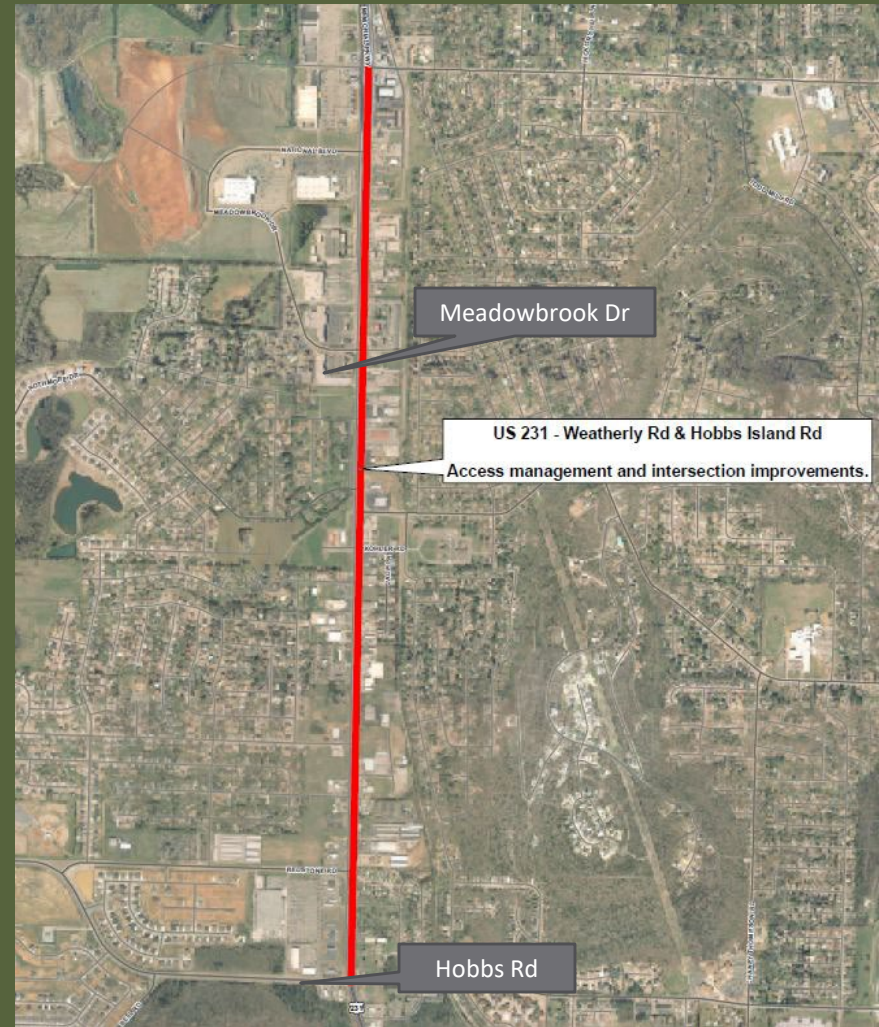



# Winchester Road from Dominion Circle to Naugher Road

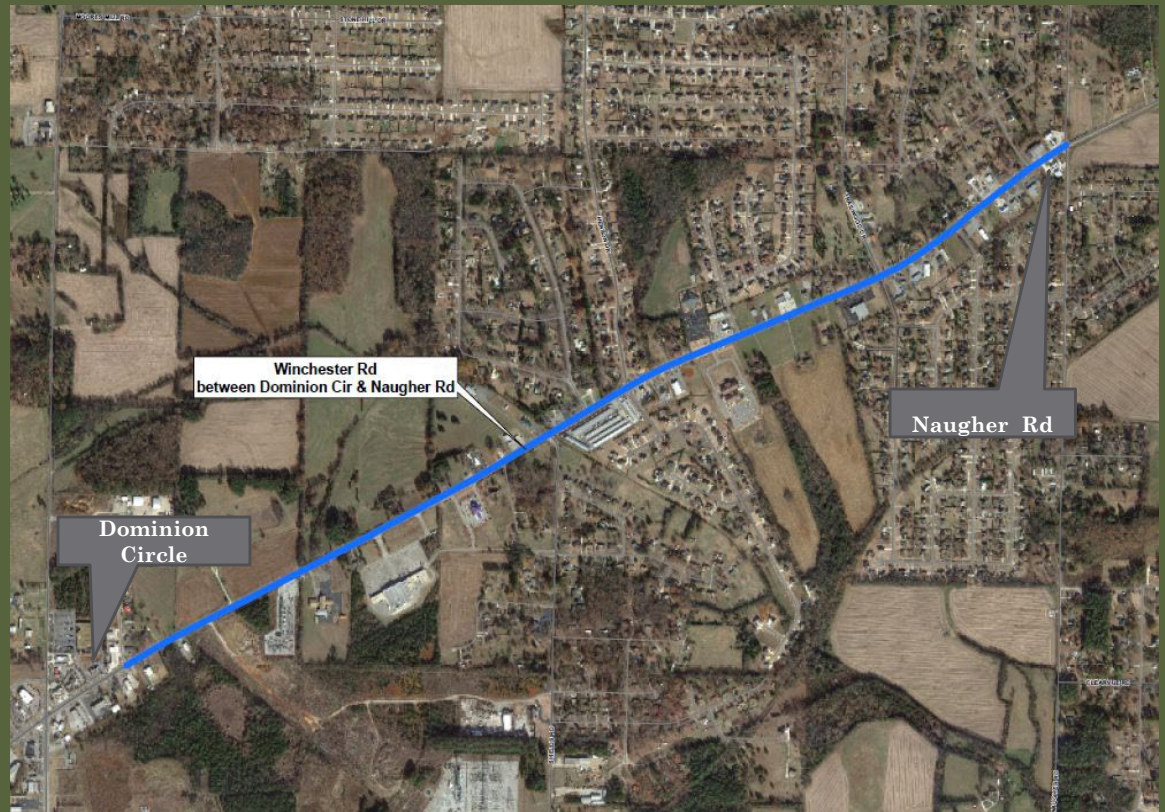


Status: Plans are 90% complete. Right-of Way Acquisition ongoing.  
Utility relocation design work to begin soon.

Estimated Cost: \$28,000,000

Anticipated Start Date: FY 2026

# US 72 West between Providence Main and County Line Road

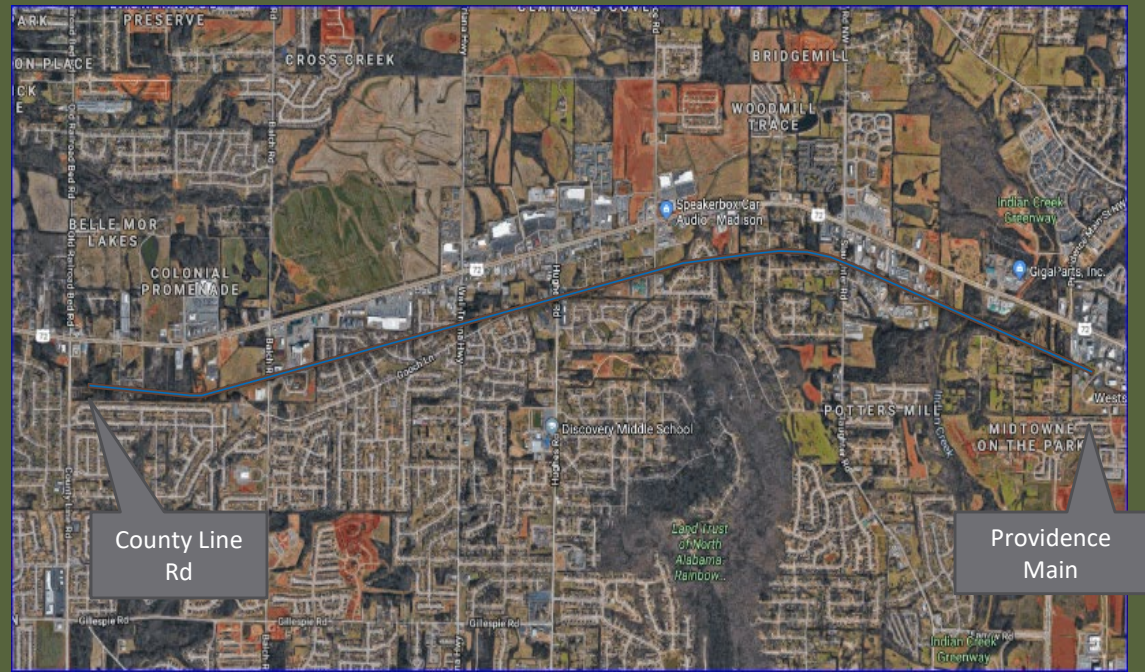

## Phase I – Huntsville Memorial Gardens to Providence Main


Status: Draft EA (environmental document) to be submitted soon.

Phase I: FY 2027 (Plans 90% complete)

Estimated Cost: \$18,000,000



# US 72 West between Providence Main and County Line Road

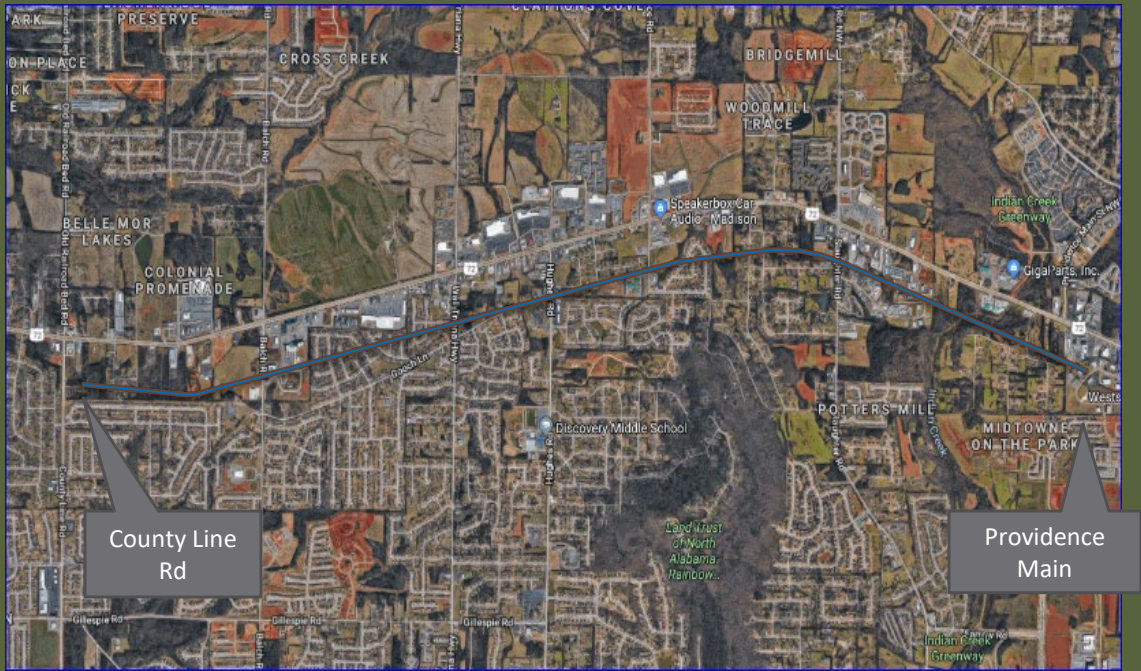

## Phase II – Walnut Street to Huntsville Memorial Gardens

Status: Preliminary Engineering authorized, consultant under contract to complete design. Construction scheduled for FY 2029

Estimated Cost: \$36,000,000



# US 72 West between Providence Main and County Line Road



## Phase III – County Line Road to Walnut Street

Status: Preliminary Engineering scheduled to start FY 25, Construction planned for FY 2030

Estimated Cost: \$38,200,000

# SR-53 Widening from Taurus Drive to Harvest Road

Status: Plans complete, ROW  
Acquisition on-going, Utility  
relocation underway.

Estimated Cost: \$10,000,000

Anticipated Start Date: FY 2025





# Madison Boulevard from Westchester Road to Flagstone Drive



Status: Project is approximately 95% complete.

Estimated Cost: \$4,200,000

# I-565 Additional Lanes from County Line Road to Wall-Triana Highway




Status: Contractor working west to east on project. Bridge Contractor is working on bridges over Intergraph Way. The project is approximately 15 % complete.

Estimated Cost: \$41,800,000



# Jeff Rd Additional Lanes from South of Capshaw Road to North of Douglas Rd

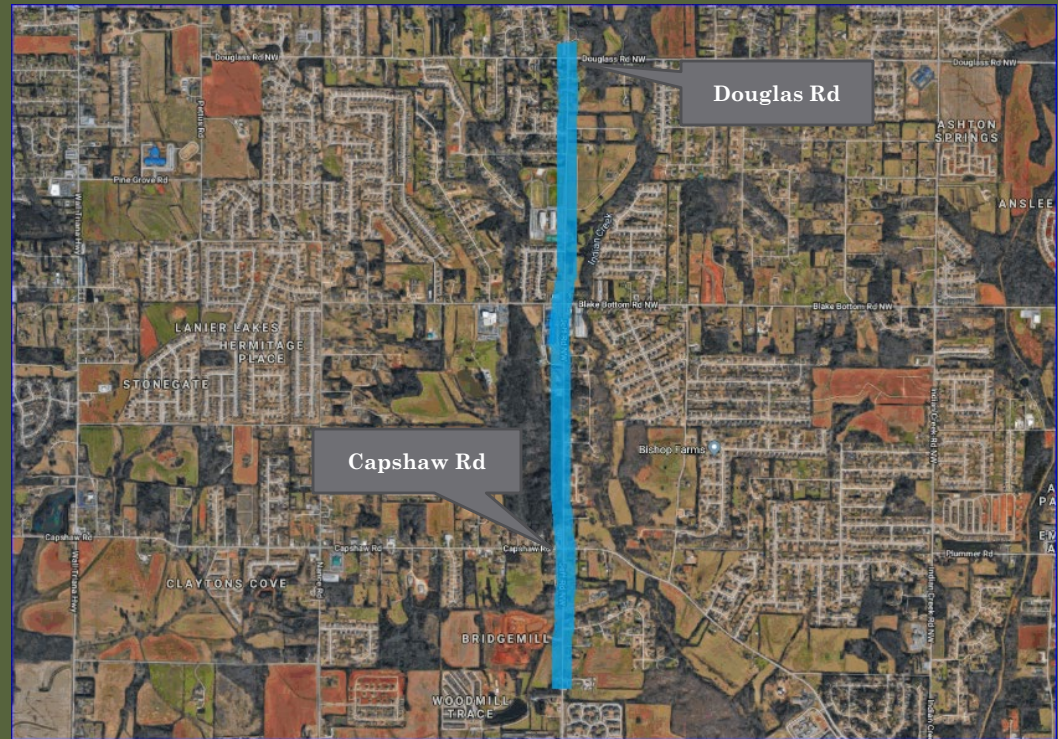


Status: Plans 85% complete, environmental document approved.  
ROW acquisition anticipated to begin this year.

Projected Start Date: FY 2026

Estimated Cost: \$13,500,000



# Widening Blake Bottom Road from Jeff Road to SR 255

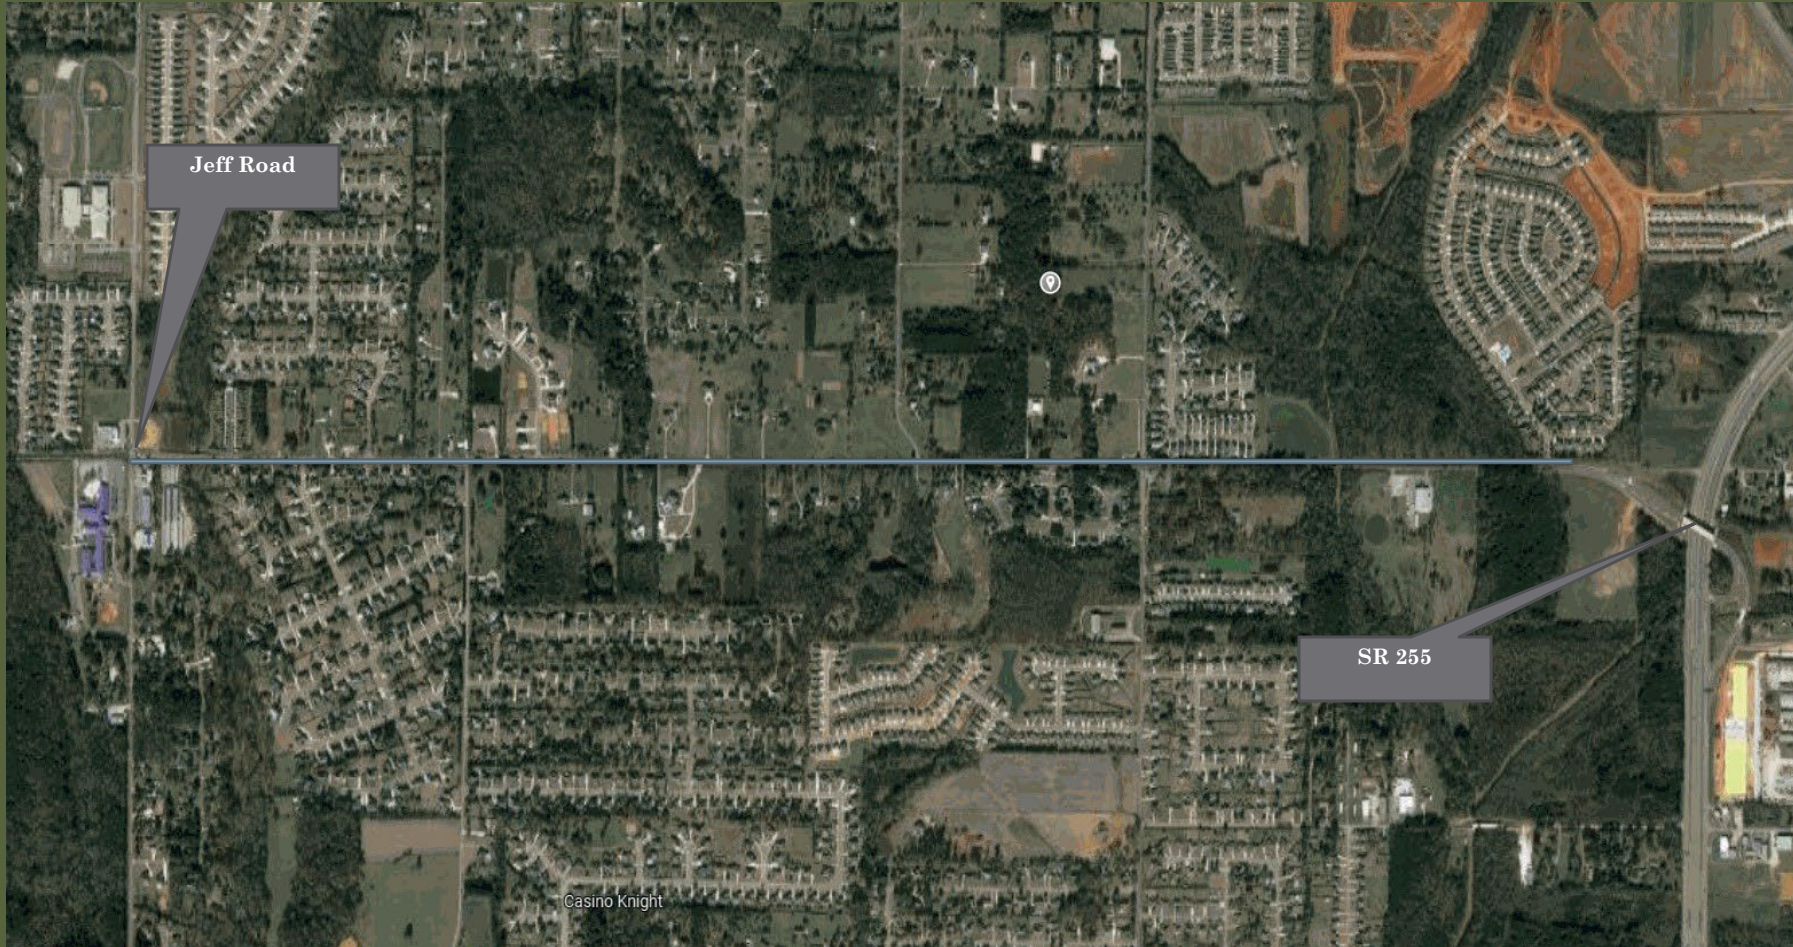

Status: Plans and ROW acquisition complete. Utility work is underway. Construction project to be bid by county later this year.

Estimated Cost: \$20,805,000

Anticipated Start Date: FY 2026



# Intersection Improvements on SR 53 at Harvest, McKee and Old Railroad Bed Roads

Harvest Road



Old Railroad Bed Road



McKee Road

Status: Work underway, approximately 75% complete.

Project Cost: \$3,700,000

# Arsenal East Connector

Bob Wallace Avenue

Goss Road

Patton Road




Status: Preliminary Engineering underway.

Estimated Cost: \$30,000,000

Anticipated Start Date: FY 2028



# I-565/Memorial Parkway Interchange Modification Study

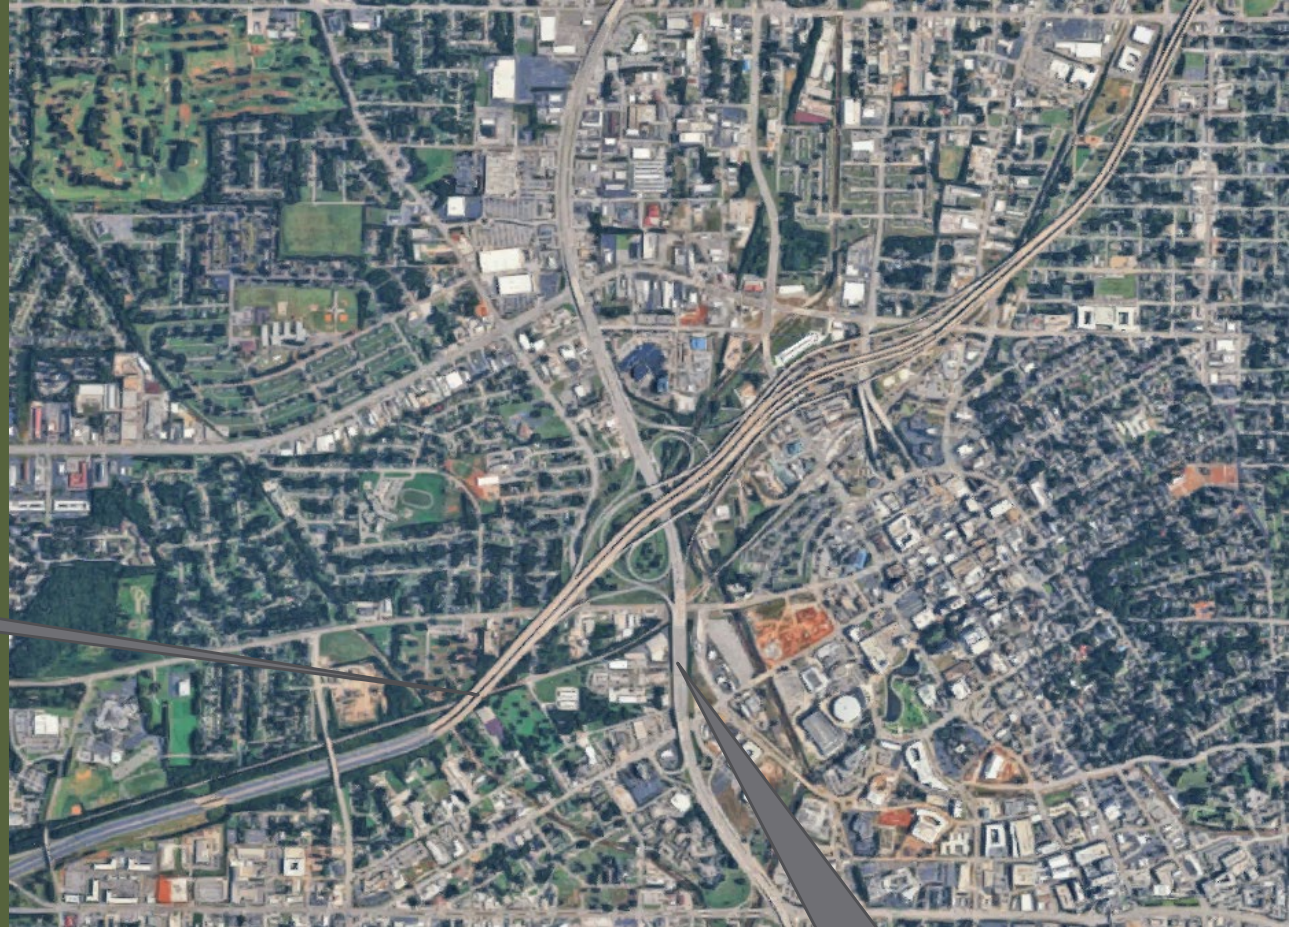

I-565

Memorial Parkway

Status: The consultant is under contract.

Estimated Cost: \$1,500,000

**Total Amount of Work in Design and  
Construction**

**\$389,905,000**
